

Summary Report

Recovery Aceh Nias Database

1 December 2005



~ Badan Rehabilitasi dan Rekonstruksi (BRR) NAD - Nias ~

RAN Database Summary Report



Table of Contents

#	Section	Page
1.	Introduction	2
2.	Organisations and Projects involved in Recovery	3
3.	BRR Outreach Campaign	3
4.	Project Costs in Aceh and Nias	4
5.	Themes of the Recovery Process	4
6.	Factors Delaying Progress	4
7.	Funds Committed and Disbursed by Sector	5
8.	Funds Committed and Disbursed by Location	5
9.	Project and Financial Information by Sector	6
10.	Project and Financial Information by Kabupaten	6
11.	Key Performance Indicators	7
12.	Key Performance Indicators by Tsunami-affected Kabupatens	9
13.	Projects by Implementing Partner	16
14.	Organisations represented in RAN Database	33



RAN Database Summary Report

1. Introduction

Throughout November, BRR and the recovery community have made a concerted effort to ensure that concept notes and progress monitoring data can be entered into the Recovery Aceh Nias (RAN) database.

In recognition of the technical difficulties of the system and the burden of first round data entry, BRR established an outreach team and data entry unit to support the recovery community in meeting their reporting obligations. 129 organisations visited the Drop In Centre and a further 174 were assisted by telephone during the data collection period.

This, the first RAN Summary Report, has been developed to give an overview of the data available in the RAN and the kind of analysis that will be possible in the coming months. The Summary Report, District Reports and Sector Reports, have been formulated to ensure that data is readily available to the relevant Government institutions and recovery community for planning, implementation and validation.

However, the data in the report should be used with caution. It is valid as of 1st December 2005 and the data and data quality is constantly improving as data submission continues. While 509 organisations are represented in the RAN, the dataset is still very much incomplete. As the reports recognize only approved concept notes, new concept notes submitted after the recent approval workshop are not included. This data will however be included in the next report. Data collection to date has focused on activity data, financial data is therefore undergoing review and validation. For clarification on the data, contact Pak Dharma Nursani, Head of Operation Centre, BRR.

BRR and the recovery community must work in partnership to ensure that the potential of the RAN is fully realized. The lessons learnt from the data collection phase will be used to improve the functionality of the database to ensure continuous development of the system to meet the needs of the entire recovery community.

BRR would like to extend its thanks to all organizations that recognize the common value in data sharing.

The **Recovery Aceh Nias (RAN) Summary Report** is a compilation of concept note and project monitoring data submitted by the recovery community of Aceh and Nias to the RAN database during 2005.

The RAN database is the official information management system of the Government of Indonesia, managed by the Government Agency for Rehabilitation and Reconstruction (BRR) and supported by the United Nations. The on-line database aims to ensure coordination in the allocation of assistance and resources; identify bottlenecks in procedures in order to analyse and resolve root causes; and enable appropriate planning for the coming months of recovery.

It is mandatory for organizations implementing projects in Aceh and Nias to report progress in the RAN database by the end of each month.


For information regarding the reporting requirements of implementing agencies in Aceh and Nias please contact the BRR Outreach Team: outreach@brr.go.id, +62(0)8136044309, +62(0)81360489818

The RAN database can be accessed through <http://www.e-aceh-nias.org>


RAN Database Summary Report

2. Organisations and Projects Involved in Recovery

Since 16th June 2005, 671 projects have been reviewed by BRR as part of the approval process. 607 are approved, 52 are in the holding bay requiring more information before approval and 12 have been rejected. There are 111 projects in the database currently awaiting review (n.b. this includes the transfer of all outstanding data from the legacy system). A further 283 projects that are currently being submitted by organisations.

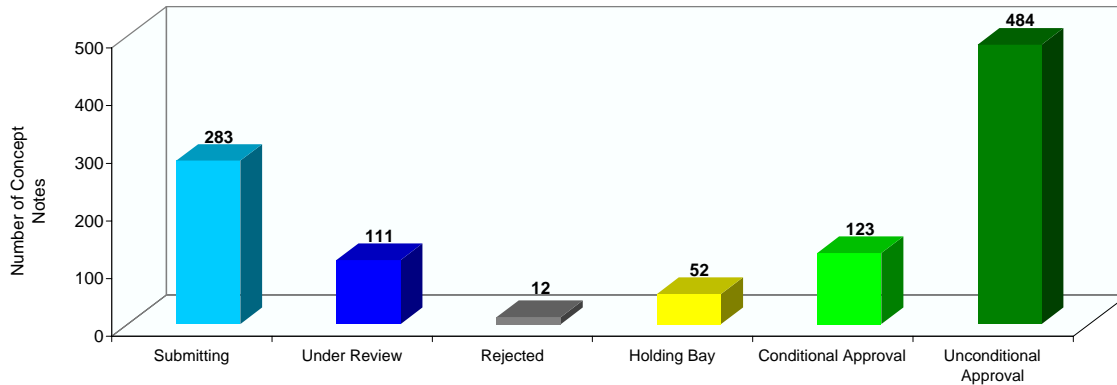


509 organisations are currently represented in the database. Of these, 251 are listed as International NGOs, 45 as National NGOs, 13 as UN Agencies, and 26 as International Organisations. A number of these organisations may not have a presence in Aceh and Nias or may no longer be working here. Please see Section 12 for a full list of organisations currently represented in the database.

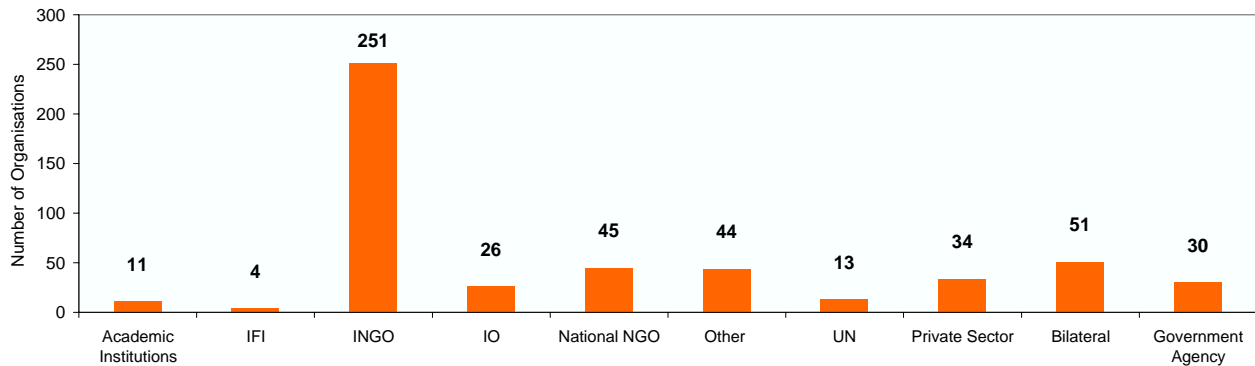

3. BRR Outreach Campaign

In recognition of the technical difficulties in data entry, BRR established an Outreach team to support the recovery community. This team gave presentations at Sector Working Groups in Banda Aceh and at Coordination Meetings in Calang, Meulaboh and Nias. The team also setup workshops with individual agencies and supported organisations on a one to one basis throughout the data entry process. As a consequence, 179 organisations have been directly contacted, 156 organisations now have a username and 129 organisations visited the Drop In Centre to use the facilities and consult with the Outreach team to input their data. By the 1st of December 50 organisations submitted a new Concept Note and 79 organisations updated their progress.




~ Figures from Outreach Campaign, 28th November to 1st December 2005 ~


RAN Database Summary Report

4. Project Costs in Aceh and Nias

For Aceh and Nias, the total cost of projects currently represented in the database is US\$2.8 billion. The six largest sectors are shown below. See map 1 for a view of the spread of total project cost across Aceh and Nias. Please note that all financial data in the RAN Database is currently under validation.

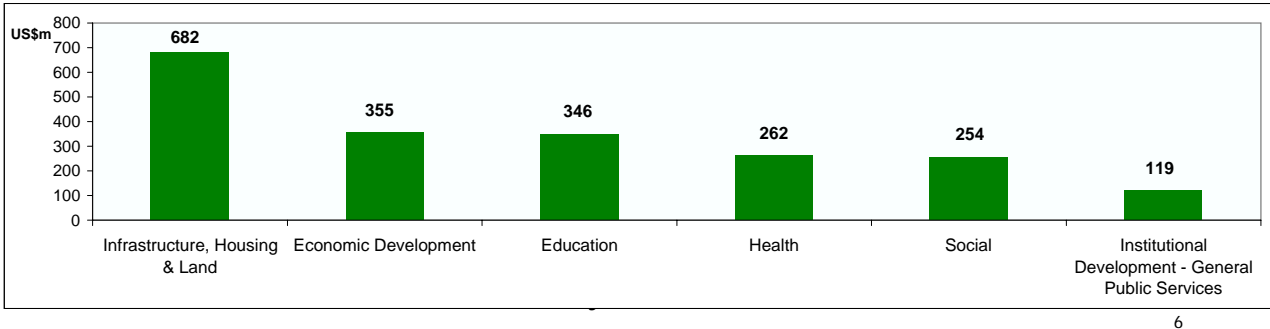


Specifically for Nias, the total cost of projects currently represented in the database is US\$89m. The six largest sectors are shown below:

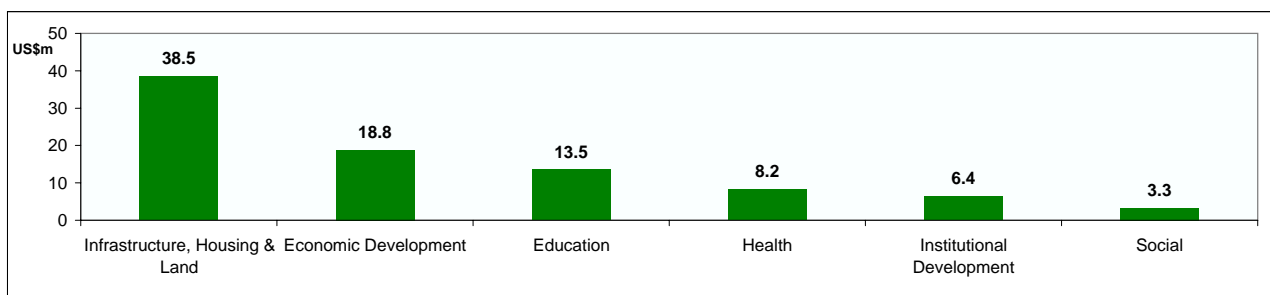


5. Themes of the Recovery Process

632 projects reported on one or more cross-cutting themes of the recovery process. Of these, 203 projects listed the promotion of community participation and 197 listed employment generation as a benefit from their work.

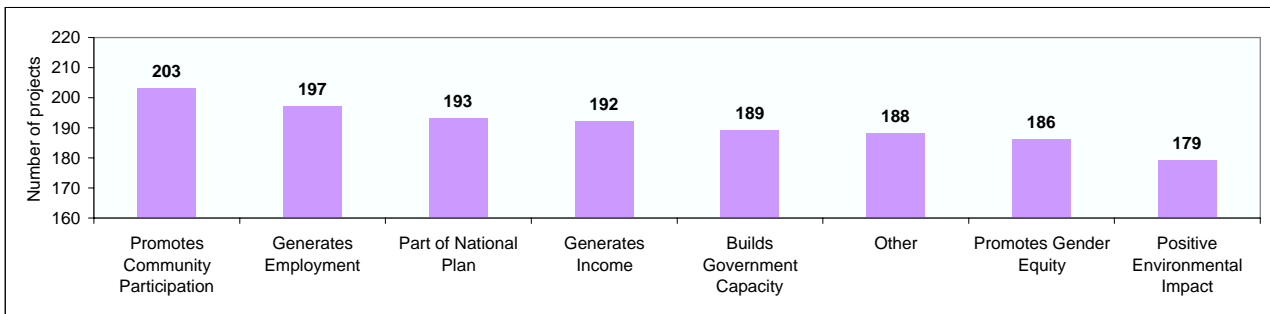

6. Factors Delaying Progress


Factors delaying progress assist BRR in identifying bottlenecks in the recovery process and in working with the provincial government to resolve the root causes. The most frequently cited factor causing delay to project implementation is 'Lack of Human Resources' (10 projects).

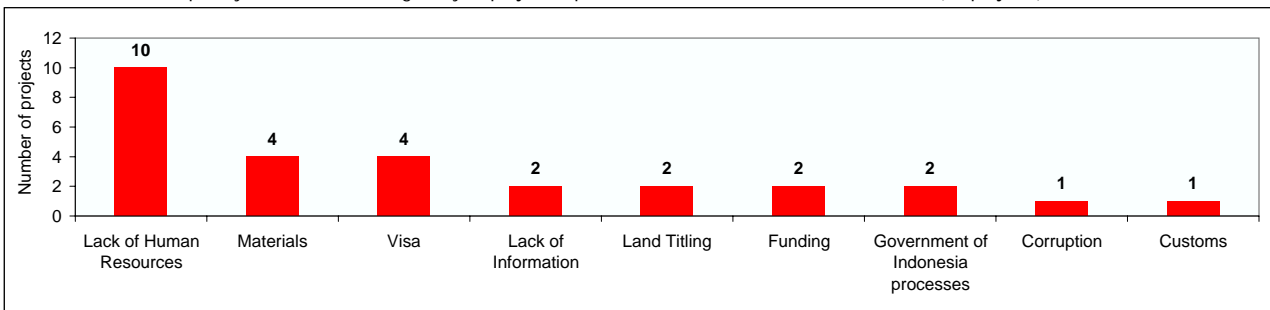

RAN Database Summary Report


7. Funds Committed and Disbursed by Sector

For Aceh and Nias, there are US\$2,082m funds committed and US\$362m already disbursed by donors that are currently represented in RAN Database. The largest sectors are shown below. Note that all financial data is currently under validation.

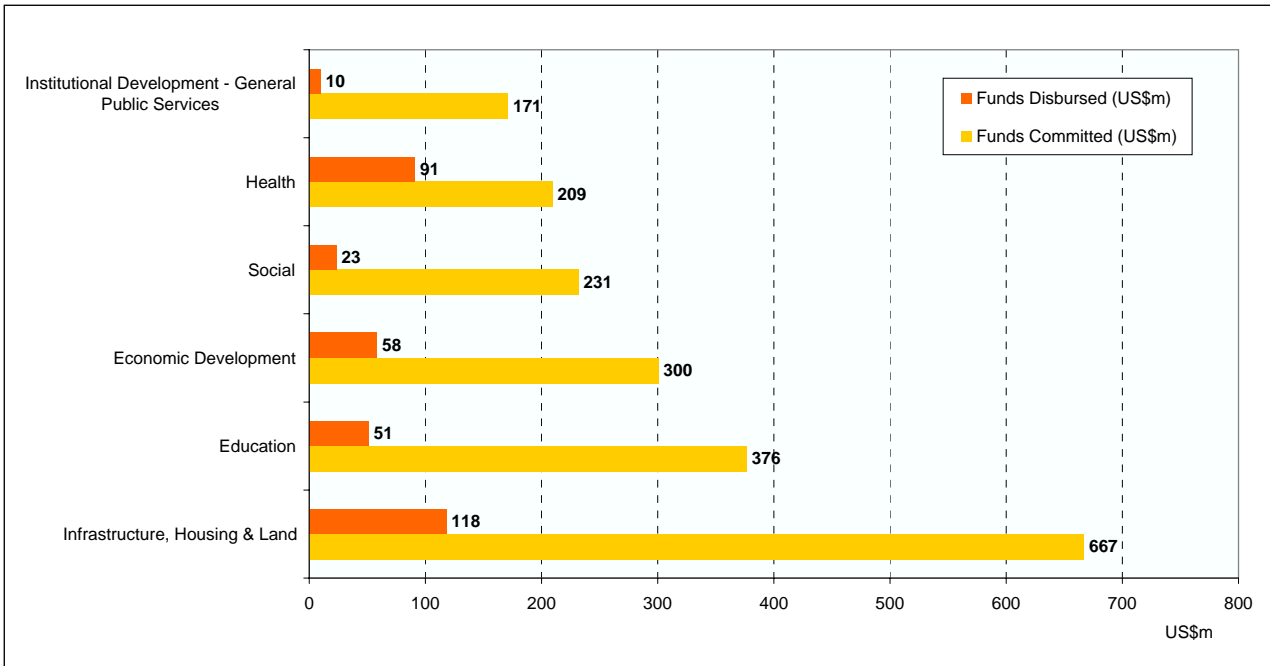

8. Funds Committed and Disbursed by Tsunami Affected Location

Total funds committed and disbursed by donors across Aceh are shown below. Banda Aceh has the most funds committed (US\$496m) and the most already disbursed (US\$78m) according to the current dataset. Note that all financial data is currently under validation.

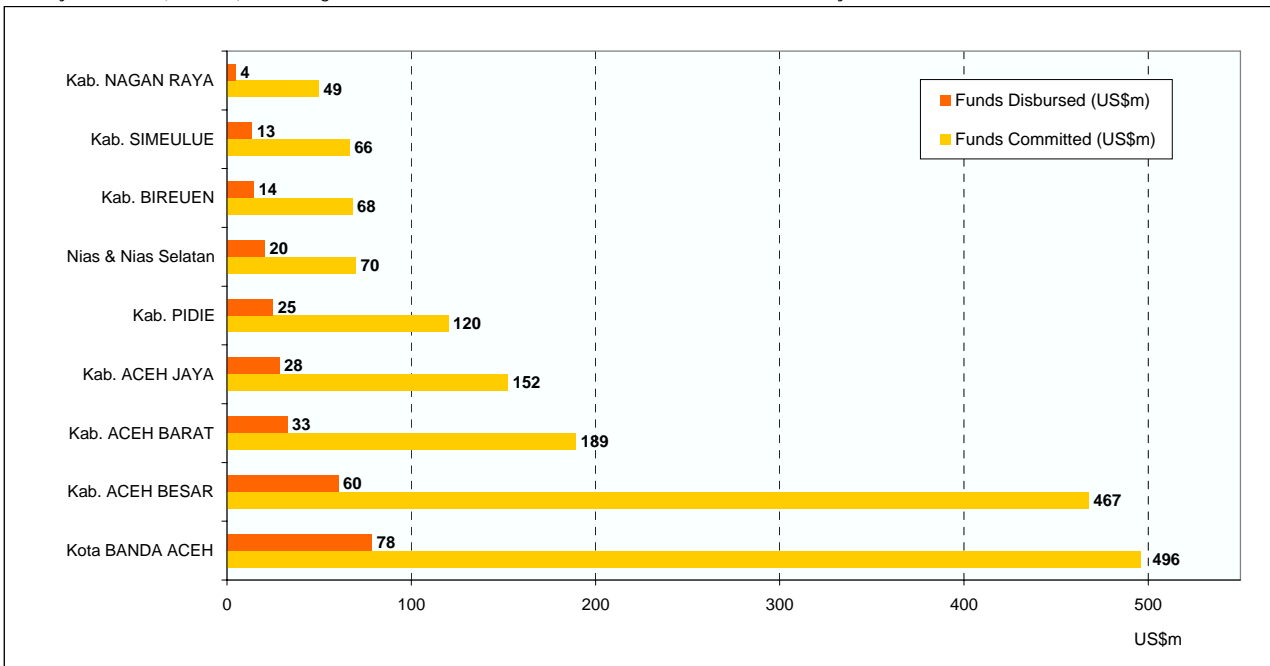

RAN Database Summary Report

9. Project and Financial Information by Sector

The first cut of financial information represented here is sourced from the database on the 1st of December. All data is currently under validation. Please see map 2 for the spread of organisations and projects across Aceh and Nias.

Sector	# of Projects	# of Organisations	Project Cost (US\$)	Funds Committed (US\$)	Funds Disbursed (US\$)
Administrative and Other Costs	5	5	996,802	978,624	866,533
Economic Development	287	134	355,374,771	300,381,561	58,116,651
Education	227	107	346,436,667	376,353,338	50,863,650
Health	172	79	261,808,849	208,963,603	91,037,432
Infrastructure, Housing & Land	339	138	681,576,103	666,788,707	117,908,207
Institutional Development - Defense	3	3	3,810,750	3,716,289	3,845
Institutional Development - General Public Services	123	68	119,382,916	170,852,427	9,696,968
Institutional Development - Public Order and Safety	23	20	27,556,118	23,461,043	854,871
Religion	26	14	31,205,329	22,762,427	980,424
Social	176	89	253,512,884	231,336,444	23,201,610
Spatial planning	44	28	36,413,094	23,766,509	3,268,497
SECTOR TO BE DEFINED	15	11	723,101,788	52,785,165	5,458,622
Total	661	208	2,841,176,071	2,082,146,137	362,257,310

10. Project and Financial Information by Kabupaten

The first cut of financial information represented here is sourced from the database on the 1st of December. All data is currently under validation.

Sector	# of Projects	# of Organisations	Project Cost (US\$)	Funds Committed (US\$)	Funds Disbursed (US\$)
All Kabupatens - All Provinces	16	13	604,528,206	17,130,485	1,177,849
Kab. ACEH BARAT	102	57	214,125,874	189,075,904	32,510,399
Kab. ACEH BARAT DAYA	9	7	9,279,320	8,253,977	984,550
Kab. ACEH BESAR	266	107	310,408,697	467,328,742	60,163,153
Kab. ACEH JAYA	84	51	185,953,427	152,057,071	28,115,891
Kab. ACEH SELATAN	13	12	20,146,199	16,616,635	840,205
Kab. ACEH SINGKIL	10	7	23,775,192	21,355,626	1,331,986
Kab. ACEH TAMIANG	2	2	3,660,190	3,660,190	0
Kab. ACEH TENGAH	6	8	7,204,209	5,430,856	149,657
Kab. ACEH TENGGARA	2	2	2,761,960	2,455,880	10,880
Kab. ACEH TIMUR	11	8	14,707,265	15,146,031	4,028,481
Kab. ACEH UTARA	38	22	49,017,152	40,727,212	9,874,162
Kab. BENER MERIAH	4	6	7,389,273	5,553,809	4,779
Kab. BIREUEN	52	33	69,838,246	67,727,067	14,239,024
Kab. GAYO LUES	2	2	2,451,123	2,449,779	4,779
Kab. NAGAN RAYA	40	26	55,389,487	49,499,695	4,276,272
Kab. NIAS	53	32	82,175,490	62,986,539	19,044,034
Kab. NIAS SELATAN	7	7	7,165,783	6,642,592	1,165,784
Kab. PIDIE	76	46	140,978,321	119,821,983	24,685,994
Kab. SIMEULUE	27	19	76,380,950	66,149,894	13,454,305
Kota BANDA ACEH	203	91	647,160,549	495,502,744	78,283,857
Kota LANGSA	2	2	1,654,773	1,663,565	448,375
Kota LHOKSEUMAWE	18	14	20,600,776	11,239,099	5,864,657
Kota SABANG	18	13	15,274,557	11,730,671	3,910,195
Kabupaten to be Defined - All Provinces	71	39	269,149,052	241,940,091	57,688,042
Total	661	208	2,841,176,071	2,082,146,137	362,257,310

CAUTION : First Data Collection Round.
Validation in progress.

RAN Database Summary Report

11. Key Performance Indicators

The indicators listed here are sourced from the database on the 1st of December. All data is currently under validation

Sector / Key Performance Indicator	Progress to date	Target from Concept Note
Economic Development		
Amount of seeds and fertilizer provided (Kg)	102,446	221,874
Area of agricultural land rehabilitated (Hectares)	1,243	5,569
Area of fish breeding areas and fishponds restored (Hectares)	70	510
Area of forest protected / rehabilitated	40	107
Area of mangrove restored (Hectares)	13	55
Area of natural habitats (wetland, mangroves, corals) restored (Hectares)	18	1,343
Employment programme implemented - number of beneficiaries	591	1,581
Length of irrigation canal new/ rehabilitated (km)	0	9
Number of industrial facilities established	1	32
Number of beneficiaries of vocational training	1,864	202,264
Number of fishing vessels provided / replaced	874	2,570
Number of industrial / agricultural machines provided	2,226	2,391
Number of loans provided to small enterprises (<50 staff)	133	1,474
Number of micro business units established	936	8,252
Number of participants in short-cycle skills and vocational training courses	2,932	6,725
Number of people placed for either permanent or temporary jobs (cash for work)	13,302	16,841
Number of traditional markets established	0	164
Sustainable employment programme implemented-number of beneficiaries	16,943	17,654
Education		
Number of books provided	72,203	78,203
Number of classrooms provided with furniture	30	30
Number of elementary schools built / repaired	19	60
Number of junior high schools built / repaired	3	9
Number of kindergarten built / repaired	18	23
Number of scholarships provided	0	3,588
Number of schools equipped with sanitation facilities	25	35
Number of schools equipped with water facilities	10	13
Number of senior high schools built / repaired	7	9
Number of teachers trained	507	1,105
Number of universities built / repaired	0	1
Health		
Assessment activities (Number)	96	96
Capacity Building-Other-program (Number of Beneficiaries)	22,605	53,039
Equipment & Supplies- Medical - Consumable (Value USD)	124,114	566,742
Equipment & Supplies- Medical - Non Consumable (Value USD)	299,245	461,905
Equipment & Supplies- Non Medical - Information & Communication Technology (Value USD)	620	1,500
Equipment & Supplies- Non Medical - Transportation (Value USD)	81,373	85,005
Equipment & Supplies- Others (Value USD)	23,951	2,049,299
Rehabilitation & Reconstruction-Hospitals (Number built/repaired)	4	13
Rehabilitation & Reconstruction-Others (Number built/repaired)	8	26
Rehabilitation & Reconstruction-Polindes (Number built/repaired)	24	77
Rehabilitation & Reconstruction-Puskesmas (Number built/repaired)	30	34
Rehabilitation & Reconstruction-Pustu (Number built/repaired)	18	24
Rehabilitation & Reconstruction-Satellite Health Posts (Number provided)	44	86
Service-CDC-Diarrhea-Program (Number of Beneficiaries)	33	33
Service-CDC-Disease Surveillance-Program (Number of Beneficiaries)	20,295	20,295
Service-CDC-EPI-Program (Number of Beneficiaries)	16,118	16,118
Service-CDC-Malaria-Program (Number of Beneficiaries)	4,250	21,005
Service-CDC-Others-Program (Number of Beneficiaries)	4,000	4,000
Service-CDC-TBC-Program (Number of Beneficiaries)	4,292	4,292
Service-Environmental Health-Health Care Waste Management-Program (Number of Beneficiaries)	20	20
Service-Environmental Health-Others-Program (Number of Beneficiaries)	900	900
Service-Health Promotion-Program (Number of Beneficiaries)	33,606	70,361
Service-MCH-Child and Adolescent-Program (Number of Beneficiaries)	7,972	10,923
Service-MCH-Reproductive Health-Program (Number of Beneficiaries)	7,023	140,073
Service-Mental Health-Program (Number of Beneficiaries)	23,556	30,184
Service-Nutrition-Program (Number of Beneficiaries)	7,806	7,806
Service-Other Curative-Program (Number of Beneficiaries)	80,039	122,695
Service-Others-Program (Number of Beneficiaries)	70,734	71,380

CAUTION: First Data Collection Round.
Validation in progress.

RAN Database Summary Report

Sector / Key Performance Indicator	Progress to date	Target from Concept Note
Training-CDC Service (Number of Personnel Trained)	780	4,097
Training-Environmental Health-Service (Number of Personnel Trained)	31	50
Training-Health Promotion (Number of Personnel Trained)	309	3,479
Training-MCH Service (Number of Personnel Trained)	1,021	8,096
Training-Mental Health Service (Number of Personnel Trained)	421	441
Training-Nutrition Service (Number of Personnel Trained)	225	225
Infrastructure, Housing & Land		
Area covered by flood control / coastal protection (km2)	0	8,041
Length of airstrip constructed / rebuilt (km)	0	2
Length of bridges built (m)	0	0
Length of roads rebuilt / constructed (km)	5	902
Number of (large-scale) water systems restored	4	20
Number of (small-scale) water points rehabilitated or constructed	375	522
Number of bridges rebuilt	4	30
Number of electrical distribution facilities rehabilitated	0	10
Number of ground water wells purified	850	2,797
Number of houses built/repared	5,778	52,704
Number of houses occupied	50	3,051
Number of houses supplied with sewage/sanitation	33	447
Number of houses supplied with water	1,988	3,992
Number of land titles issued	464	2,523
Number of latrines built	617	1,556
Number of office buildings built / repaired	0	1
Number of ports / harbours redeveloped	0	1
Number of public buildings built / repaired	3	15
Number of sanitation schemes restored	365	1,648
Number of temporary houses built	595	1,655
Number of water distribution facilities rehabilitated	476	3,375
Institutional Development - Defense		
Number of civil servants who have received training	0	0
Institutional Development - General Public Services		
Number of civil servants training courses assessed and strengthened	0	0
Number of compliance guidelines developed for local government	0	0
Number of monitoring arrangements developed to ensure compliance with relevant standards and guidelines	30	32
Institutional Development - Public Order and Safety		
Number of facilitators recruited for community participation and empowerment	0	30
Religion		
Number of mosques built / repaired	0	5
Number of pesantren (religious schools) built / repaired	1	2
Social		
Number of community initiative discussion groups established	39	356
Number of community/village halls rebuilt/new	74	117
Number of cultural performances / exhibitions conducted	121	133
Number of cultural/training workshops	36	504
Number of integrated community based women's centres established	132	220
Number of musuems, libraries and other cultural facilities built / repaired	1	3
Number of people trained (e.g. community leadership, peace education, social research methodology)	550	2,940
Number of proposals implemented to commemorate the tsunami	8	8
Number of public reading parks established	0	2
Number of sport facilities rehabilitated	18	25
Number of women receiving legal assistance	50	50
Number of women receiving livelihood capacity training	555	2,490
Spatial planning		
Number of villages where marking of property boundaries completed	0	0
Number of villages where village layout drawing completed	0	0

RAN Database Summary Report

12. Key Performance Indicators by Tsunami-affected Locations

The indicators listed here are sourced from the database on the 1st of December. All data is currently under validation

Kabupaten / Indicator	No of Projects	Progress	Target
Kab. ACEH BARAT			
Economic Development			
Employment programme implemented - number of beneficiaries	1	0	0
Number of beneficiaries of vocational training	1	925	925
Number of fishing vessels provided / replaced	2	82	82
Number of industrial / agricultural machines provided	1	4	4
Number of micro business units established	2	12	312
Number of participants in short-cycle skills and vocational training courses	1	0	450
Number of people placed for either permanent or temporary jobs (cash for work)	4	2,822	3,722
Sustainable employment programme implemented-number of beneficiaries	1	1,120	1,120
Education			
Number of books provided	3	326	326
Number of elementary schools built / repaired	2	5	9
Number of kindergarten built / repaired	3	1	2
Number of schools equipped with sanitation facilities	1	10	14
Number of senior high schools built / repaired	1	1	2
Number of teachers trained	2	18	194
Infrastructure			
Length of roads rebuilt / constructed (km)	2	0	220
Number of (large-scale) water systems restored	1	0	0
Number of (small-scale) water points rehabilitated or constructed	4	60	67
Number of houses built/repared	9	322	9,307
Number of houses supplied with water	1	150	200
Number of land titles issued	3	162	1,729
Number of latrines built	3	64	91
Number of public buildings built / repaired	1	0	0
Number of sanitation schemes restored	2	154	154
Number of water distribution facilities rehabilitated	1	0	0
Institutional Development - General Public Services			
Number of compliance guidelines developed for local government	1	0	0
Social			
Number of community initiative discussion groups established	1	0	36
Number of community/village halls rebuilt/new	2	6	28
Number of cultural performances / exhibitions conducted	1	7	19
Number of cultural/training workshops	2	11	479
Number of people trained (e.g. community leadership, peace education, social research methodology)	3	48	1,637
Number of sport facilities rehabilitated	1	3	3
Number of women receiving livelihood capacity training	1	0	450
Health			
Equipment & Supplies- Medical - Consumable (Value USD)	2	15,000	60,000
Equipment & Supplies- Medical - Non Consumable (Value USD)	1	30,000	30,000
Equipment & Supplies- Others (Value USD)	1	14,299	14,299
Rehabilitation & Reconstruction-Others (Number built/repared)	2	0	0
Rehabilitation & Reconstruction-Satellite Health Posts (Number provided)	1	0	0
Service-MCH-Child and Adolescent-Program (Number of Beneficiaries)	1	3,026	3,026
Service-MCH-Reproductive Health-Program (Number of Beneficiaries)	1	610	610
Service-Mental Health-Program (Number of Beneficiaries)	1	0	0
Service-Nutrition-Program (Number of Beneficiaries)	1	4,974	4,974
Training-CDC Service (Number of Personnel Trained)	1	82	332
Training-Health Promotion (Number of Personnel Trained)	1	10	10
Training-MCH Service (Number of Personnel Trained)	1	141	141

CAUTION: First Data Collection Round.
Validation in progress.

RAN Database Summary Report

Kabupaten / Indicator	No of Projects	Progress	Target
Kab. ACEH JAYA			
Economic Development			
Amount of seeds and fertilizer provided (Kg)	2	59,096	128,233
Area of agricultural land rehabilitated (Hectares)	6	1,114	2,909
Area of forest protected / rehabilitated	2	40	107
Employment programme implemented - number of beneficiaries	1	10	10
Number of beneficiaries of vocational training	1	939	939
Number of fishing vessels provided / replaced	2	275	275
Number of industrial / agricultural machines provided	1	2,214	2,214
Number of micro business units established	2	280	468
Number of people placed for either permanent or temporary jobs (cash for work)	5	2,623	2,633
Sustainable employment programme implemented-number of beneficiaries	1	3,878	3,878
Education			
Number of books provided	2	18,622	18,622
Number of classrooms provided with furniture	1	11	11
Number of elementary schools built / repaired	1	5	6
Number of junior high schools built / repaired	1	1	1
Number of kindergarten built / repaired	2	6	6
Number of schools equipped with sanitation facilities	1	4	4
Number of schools equipped with water facilities	1	2	2
Number of teachers trained	1	0	106
Infrastructure			
Length of roads rebuilt / constructed (km)	4	0	227
Number of (large-scale) water systems restored	1	0	4
Number of (small-scale) water points rehabilitated or constructed	3	115	115
Number of ground water wells purified	2	609	609
Number of houses built/repared	6	151	3,553
Number of houses supplied with sewage/sanitation	1	0	409
Number of houses supplied with water	1	0	409
Number of land titles issued	2	0	429
Number of latrines built	3	379	391
Number of ports / harbours redeveloped	1	0	0
Number of public buildings built / repaired	1	3	3
Number of sanitation schemes restored	4	4	6
Number of temporary houses built	3	153	747
Number of water distribution facilities rehabilitated	1	1	1
Social			
Number of community initiative discussion groups established	1	4	4
Number of community/village halls rebuilt/new	2	1	1
Number of cultural performances / exhibitions conducted	1	1	1
Number of cultural/training workshops	1	1	1
Number of integrated community based women's centres established	1	126	126
Number of people trained (e.g. community leadership, peace education, social research methodology)	2	49	67
Number of sport facilities rehabilitated	1	7	7
Number of women receiving legal assistance	1	50	50
Number of women receiving livelihood capacity training	1	266	266

RAN Database Summary Report

Kabupaten / Indicator	No of Projects	Progress	Target
Health			
Assessment activities (Number)	3	32	32
Capacity Building-Other-program (Number of Beneficiaries)	2	22,187	22,187
Equipment & Supplies- Medical - Consumable (Value USD)	5	18,714	86,742
Equipment & Supplies- Medical - Non Consumable (Value USD)	4	18,745	71,204
Equipment & Supplies- Non Medical - Information & Communication Technology (Value USD)	1	620	1,500
Equipment & Supplies- Non Medical - Transportation (Value USD)	2	31,373	35,005
Equipment & Supplies- Others (Value USD)	1	9,652	35,000
Rehabilitation & Reconstruction-Others (Number built/repared)	2	4	4
Rehabilitation & Reconstruction-Polindes (Number built/repared)	2	1	2
Rehabilitation & Reconstruction-Puskesmas (Number built/repared)	4	4	5
Rehabilitation & Reconstruction-Pustu (Number built/repared)	3	3	4
Rehabilitation & Reconstruction-Satellite Health Posts (Number provided)	2	4	4
Service-CDC-Disease Surveillance-Program (Number of Beneficiaries)	1	4,247	4,247
Service-CDC-EPI-Program (Number of Beneficiaries)	1	4,247	4,247
Service-CDC-Malaria-Program (Number of Beneficiaries)	1	4,247	4,247
Service-CDC-TBC-Program (Number of Beneficiaries)	2	4,292	4,292
Service-Health Promotion-Program (Number of Beneficiaries)	1	20,000	20,000
Service-MCH-Child and Adolescent-Program (Number of Beneficiaries)	2	1,508	1,508
Service-MCH-Reproductive Health-Program (Number of Beneficiaries)	2	4,250	4,250
Service-Mental Health-Program (Number of Beneficiaries)	3	9,000	9,000
Service-Nutrition-Program (Number of Beneficiaries)	1	0	0
Service-Other Curative-Program (Number of Beneficiaries)	3	28,887	34,950
Service-Others-Program (Number of Beneficiaries)	2	22,187	22,808
Training-CDC Service (Number of Personnel Trained)	3	81	286
Training-Health Promotion (Number of Personnel Trained)	2	35	115
Training-MCH Service (Number of Personnel Trained)	3	174	189
Training-Mental Health Service (Number of Personnel Trained)	2	62	82
Kab. NAGAN RAYA			
Economic Development			
Number of fishing vessels provided / replaced	1	10	10
Sustainable employment programme implemented-number of beneficiaries	1	465	465
Education			
Number of books provided	1	18	18
Number of kindergarten built / repaired	1	4	4
Infrastructure			
Number of (small-scale) water points rehabilitated or constructed	1	5	5
Number of ground water wells purified	1	6	6
Number of houses built/repared	1	0	374
Number of land titles issued	2	0	0
Number of latrines built	1	51	51
Social			
Number of people trained (e.g. community leadership, peace education, social research methodology)	1	14	14
Number of sport facilities rehabilitated	1	2	2
Health			
Capacity Building-Other-program (Number of Beneficiaries)	1	0	9
Equipment & Supplies- Medical - Consumable (Value USD)	1	5,400	36,000
Equipment & Supplies- Medical - Non Consumable (Value USD)	2	30,000	100,000
Rehabilitation & Reconstruction-Others (Number built/repared)	1	2	2
Rehabilitation & Reconstruction-Puskesmas (Number built/repared)	1	11	11
Rehabilitation & Reconstruction-Pustu (Number built/repared)	1	0	3
Rehabilitation & Reconstruction-Satellite Health Posts (Number provided)	1	0	42
Service-MCH-Reproductive Health-Program (Number of Beneficiaries)	1	0	131,747
Training-CDC Service (Number of Personnel Trained)	1	0	285
Training-Health Promotion (Number of Personnel Trained)	2	61	76
Training-MCH Service (Number of Personnel Trained)	3	216	7,276

RAN Database Summary Report

Kabupaten / Indicator	No of Projects	Progress	Target
Kab. NIAS			
Economic Development			
Number of fishing vessels provided / replaced	1	0	1
Number of micro business units established	1	9	11
Number of participants in short-cycle skills and vocational training courses	1	0	1
Number of traditional markets established	1	0	157
Education			
Number of books provided	1	0	0
Number of elementary schools built / repaired	2	4	17
Number of junior high schools built / repaired	1	0	4
Number of schools equipped with sanitation facilities	2	4	4
Infrastructure			
Number of (large-scale) water systems restored	1	1	3
Number of (small-scale) water points rehabilitated or constructed	1	0	19
Number of bridges rebuilt	2	4	11
Number of electrical distribution facilities rehabilitated	1	0	10
Number of ground water wells purified	2	4	4
Number of houses built/repared	7	156	2,047
Number of land titles issued	6	0	0
Number of latrines built	2	50	950
Number of sanitation schemes restored	2	0	1,276
Number of temporary houses built	1	0	251
Number of water distribution facilities rehabilitated	3	0	719
Institutional Development - Public Order and Safety			
Number of facilitators recruited for community participation and empowerment	1	0	0
Social			
Number of community initiative discussion groups established	1	0	0
Number of community/village halls rebuilt/new	1	1	1
Number of people trained (e.g. community leadership, peace education, social research methodology)	2	10	10
Health			
Equipment & Supplies- Medical - Consumable (Value USD)	1	0	0
Rehabilitation & Reconstruction-Others (Number built/repared)	6	0	0
Rehabilitation & Reconstruction-Pustu (Number built/repared)	1	3	3
Rehabilitation & Reconstruction-Satellite Health Posts (Number provided)	1	32	32
Service-Health Promotion-Program (Number of Beneficiaries)	1	0	0
Service-Mental Health-Program (Number of Beneficiaries)	1	0	0
Service-Nutrition-Program (Number of Beneficiaries)	1	0	0
Training-Environmental Health-Service (Number of Personnel Trained)	1	31	50
Kab. NIAS SELATAN			
Infrastructure			
Number of houses built/repared	1	0	30

RAN Database Summary Report

Kabupaten / Indicator	No of Projects	Progress	Target
Kab. PIDIE			
Economic Development			
Area of fish breeding areas and fishponds restored (Hectares)	1	70	120
Area of mangrove restored (Hectares)	1	0	42
Employment programme implemented - number of beneficiaries	1	0	0
Length of irrigation canal new/ rehabilitated (km)	1	0	9
Number of fishing vessels provided / replaced	2	64	144
Number of micro business units established	1	0	200
Number of people placed for either permanent or temporary jobs (cash for work)	1	0	0
Sustainable employment programme implemented-number of beneficiaries	1	368	747
Education			
Number of books provided	1	1,000	1,000
Number of elementary schools built / repaired	2	0	1
Number of senior high schools built / repaired	1	5	6
Number of teachers trained	1	60	100
Infrastructure			
Length of airstrip constructed / rebuilt (km)	1	0	2
Length of roads rebuilt / constructed (km)	1	0	1
Number of (small-scale) water points rehabilitated or constructed	1	0	60
Number of bridges rebuilt	1	0	2
Number of ground water wells purified	1	0	331
Number of houses built/repared	8	223	2,065
Number of houses occupied	1	50	50
Number of houses supplied with sewage/sanitation	1	0	0
Number of office buildings built / repaired	1	0	1
Number of public buildings built / repaired	1	0	2
Number of sanitation schemes restored	1	0	1
Social			
Number of community initiative discussion groups established	1	0	40
Number of integrated community based women's centres established	2	0	20
Number of people trained (e.g. community leadership, peace education, social research methodology)	1	62	106
Number of women receiving livelihood capacity training	2	144	184
Spatial Planning			
Number of villages where marking of property boundaries completed	2	0	0
Health			
Assessment activities (Number)	1	34	34
Capacity Building-Other-program (Number of Beneficiaries)	1	416	416
Equipment & Supplies- Medical - Consumable (Value USD)	2	36,300	72,000
Equipment & Supplies- Medical - Non Consumable (Value USD)	2	84,600	84,800
Equipment & Supplies- Non Medical - Transportation (Value USD)	1	50,000	50,000
Rehabilitation & Reconstruction-Puskesmas (Number built/repared)	2	6	6
Rehabilitation & Reconstruction-Pustu (Number built/repared)	1	5	5
Rehabilitation & Reconstruction-Satellite Health Posts (Number provided)	1	3	3
Service-CDC-EPI-Program (Number of Beneficiaries)	1	10,943	10,943
Service-CDC-Others-Program (Number of Beneficiaries)	1	2,000	2,000
Service-Health Promotion-Program (Number of Beneficiaries)	2	6,995	19,985
Service-Mental Health-Program (Number of Beneficiaries)	1	9,156	15,784
Service-Other Curative-Program (Number of Beneficiaries)	1	47,070	49,825
Training-CDC Service (Number of Personnel Trained)	3	35	875
Training-MCH Service (Number of Personnel Trained)	1	59	59
Training-Mental Health Service (Number of Personnel Trained)	1	120	120
Training-Nutrition Service (Number of Personnel Trained)	1	100	100

RAN Database Summary Report

Kabupaten / Indicator	No of Projects	Progress	Target
Kota BANDA ACEH			
Economic Development			
Amount of seeds and fertilizer provided (Kg)	2	0	50,030
Area of fish breeding areas and fishponds restored (Hectares)	1	0	300
Employment programme implemented - number of beneficiaries	1	401	827
Number of beneficiaries of vocational training	1	0	200,000
Number of fishing vessels provided / replaced	1	0	103
Number of loans provided to small enterprises (<50 staff)	1	1	1
Number of micro business units established	1	0	500
Number of participants in short-cycle skills and vocational training courses	1	0	0
Number of people placed for either permanent or temporary jobs (cash for work)	4	1,100	2,200
Sustainable employment programme implemented-number of beneficiaries	1	299	299
Education			
Number of books provided	2	44,661	44,661
Number of classrooms provided with furniture	1	5	5
Number of elementary schools built / repaired	4	1	3
Number of junior high schools built / repaired	2	0	2
Number of kindergarten built / repaired	2	0	0
Number of scholarships provided	1	0	933
Number of schools equipped with sanitation facilities	2	1	4
Number of schools equipped with water facilities	1	1	1
Number of senior high schools built / repaired	1	0	0
Number of teachers trained	1	222	222
Number of universities built / repaired	2	0	1
Infrastructure			
Area covered by flood control / coastal protection (km2)	1	0	41
Length of roads rebuilt / constructed (km)	1	0	220
Number of (small-scale) water points rehabilitated or constructed	1	5	5
Number of ground water wells purified	2	110	110
Number of houses built/repaired	10	706	6,205
Number of houses occupied	1	0	1
Number of houses supplied with sewage/sanitation	1	5	5
Number of land titles issued	9	1	6
Number of latrines built	2	61	61
Number of ports / harbours redeveloped	2	0	1
Number of sanitation schemes restored	1	28	28
Number of water distribution facilities rehabilitated	4	2	202
Institutional Development - General Public Services			
Number of civil servants training courses assessed and strengthened	1	0	0
Number of compliance guidelines developed for local government	1	0	0
Institutional Development - Public Order and Safety			
Number of facilitators recruited for community participation and empowerment	2	0	30
Social			
Number of community initiative discussion groups established	2	3	64
Number of community/village halls rebuilt/new	1	36	36
Number of cultural performances / exhibitions conducted	1	0	0
Number of cultural/training workshops	1	1	1
Number of integrated community based women's centres established	1	2	12
Number of people trained (e.g. community leadership, peace education, social research methodology)	1	62	106

RAN Database Summary Report

Kabupaten / Indicator	No of Projects	Progress	Target
Health			
Assessment activities (Number)	3	21	21
Capacity Building-Other-program (Number of Beneficiaries)	6	2	764
Equipment & Supplies- Medical - Consumable (Value USD)	2	7,200	48,000
Equipment & Supplies- Medical - Non Consumable (Value USD)	2	130,000	170,000
Equipment & Supplies- Non Medical - Information & Communication Technology (Value USD)	1	0	0
Rehabilitation & Reconstruction-Hospitals (Number built/repaired)	4	1	6
Rehabilitation & Reconstruction-Others (Number built/repaired)	8	0	3
Rehabilitation & Reconstruction-Puskesmas (Number built/repaired)	2	2	2
Rehabilitation & Reconstruction-Pustu (Number built/repaired)	1	3	3
Rehabilitation & Reconstruction-Satellite Health Posts (Number provided)	1	1	1
Service-CDC-Diarrhea-Program (Number of Beneficiaries)	1	13	13
Service-CDC-Disease Surveillance-Program (Number of Beneficiaries)	1	14,349	14,349
Service-CDC-EPI-Program (Number of Beneficiaries)	1	120	120
Service-CDC-Others-Program (Number of Beneficiaries)	1	2,000	2,000
Service-Health Promotion-Program (Number of Beneficiaries)	1	1,811	9,357
Service-MCH-Child and Adolescent-Program (Number of Beneficiaries)	1	1,531	1,893
Service-MCH-Reproductive Health-Program (Number of Beneficiaries)	1	2,032	2,099
Service-Mental Health-Program (Number of Beneficiaries)	1	1,400	1,400
Service-Other Curative-Program (Number of Beneficiaries)	2	923	21,305
Service-Others-Program (Number of Beneficiaries)	1	39,075	39,075
Training-CDC Service (Number of Personnel Trained)	1	87	194
Training-Health Promotion (Number of Personnel Trained)	5	30	3,065
Training-MCH Service (Number of Personnel Trained)	1	6	6
Training-Mental Health Service (Number of Personnel Trained)	1	59	59
Training-Nutrition Service (Number of Personnel Trained)	1	30	30

RAN Database Summary Report

13. Projects by Implementing Partner

This is the list of Partner projects in the database on the 1st of December. This is currently being validated to ensure that the correct partner organisations are identified for each project. Please contact the BRR Outreach Team if your organisation's projects are not listed accurately.

Partner / Project ID	Title	Project Status
ACF		
INFRA 10 IN	Water and Sanitation	Ongoing
ECON 11 IN	Food Security	Ongoing
ACTED		
ECON 34 IN	Support to recovery of fishery economic activity in Kec. Samatiga, Kab. Aceh Barat	Ongoing
ECON 35 IN	Support to recovery of fishery economic activity in Kec. Samatiga, Kab. Aceh Barat	Ongoing
INFRA 50 IN	Emergency assistance to shelter and water and sanitation systems rehabilitation in Kec. Lahewa, Kab. Nias	Ongoing
INFRA 51 IN	Rehabilitation and support to recovery of economic activities in Kec. Kuala and Kec. Daruk Makmur, Kab. Nagan Raya and Kec. Samatiga, Kab. Aceh Barat – Agriculture, Water and Sanitation, Waste Management	Ongoing
INFRA 52 IN	Rehabilitation of water and sanitation systems in Kab. Aceh Barat and Nagan Raya	Ongoing
INFRA 93 Bilat	Emergency assistance to shelter and water and sanitation systems rehabilitation in Kec. Lahewa, Kab. Nias	Ongoing
AIFO		
HEAL 48 IN	Socio Sanitary Rehabilitation in the three districts of the Aceh Province	Ongoing
HEAL 49 IN	Rehabilitation and ampliation of two Postus in two districts of Aceh Province	Design
AIPRD		
HEAL 6 Bilat	AIPRD Aceh Rehabilitation Program: Hospital Restoration	Ongoing
EDUC 63 IN	Earthquake and Tsunami Emergency Support Project (ETESP) – Education & Skills Development Component	Completed
HEAL 5 Bilat	Health Assistance Rehabilitation Aceh Program (HARAP)	Initial Phase
INST 3 Bilat	Support to Local Governance Aceh	Completed
INST 34 BILAT	INST 34 BILAT (BATCH 10) - AIPRD Aceh Rehabilitation Program: Expanded Support for Construction	Ongoing
EDUC - 0106 - Bilat	Aceh Tertiary Education and Training Program, Universitas Syiah Kuala, Banda Aceh	Ongoing
EDUC - 0108 - Bilat	AIPRD Aceh Rehabilitation Program: Expanded Support for Construction	Ongoing
HEAL - 0116 - Bilat	AIPRD Aceh Rehabilitation Program: Expanded Support for Construction	Ongoing
AMDA		
INFRA 158 IN	Community-Based Emergency Shelter Rehabilitation (CBESR) for IDPs in Nias	Ongoing
HEAL 85 IN	Medical Emergency Response & Coordination Training (MERCT)	Design
HEAL 84 IN	Anaesthetist Support Program (ASP) under Hospital Support Program	Ongoing
HEAL 86 IN	Nurse Training Program (NTP) under Hospital Support Program	Design
AMI FRANCE		
HEAL 47 IN	Health Reconstruction	Design
AMURT		
ECON 56 IN	Organic Farming Livelihood Project	Design
EDUC 25 IN	Permanent TK Bada	Design
EDUC 26 IN	Permanent TK Peukan Bada	Completed
EDUC 27 IN	Permanent SDN1 Peukan Bada	Completed
EDUC 68 IN	Permanent TK Ujong Batee	Design
ECON 114 IN	Renovation of 2 Units in a dilapidated concrete building behind barak Raider to create a Livelihood Training Centre	Design
EDUC 83 IN	Permanent Kindergarten - Pulau Nasi	Approval
EDUC 75 IN	Seuremo SD Renovation	Design
EDUC 81 IN	Raidar Barrack TK Renovation	Design
EDUC 84 IN	Permanent Kindergarten - Tumbo Baro	Ongoing
ATLAS Logistique		
INFRA 176 IN	Logistics support (storage, boat and truck transportation) for all humanitarian organizations	Ongoing
Abdul Lateef Jamil Group		
CROSS 15 Bilat	Emergency Program to Support the Indonesian People Tsunami strike	Ongoing
Aceh Institute		
SOCI 60 UN	Multisectoral Gender needs Assesment and Situational Analysis	Ongoing
Aceh Relief		
INFRA 146 IN	ACEH RELIEF	Ongoing

RAN Database Summary Report

Partner / Project ID	Title	Project Status
Alisei		
<i>ECON 75 UN</i>	District	Design
<i>ECON 86 UN</i>	Humanitarian Emergency Aid for Communities In Pidie 1	Design
<i>ECON 87 UN</i>	Humanitarian Emergency Aid for Communities In Pidie 2	Design
<i>HEAL 50 Bilat</i>	Polindes Reconstruction/Rehabilitation Programme in Pidie District	Design
<i>INFRA 102 Bilat</i>	Permanent Houses Reconstruction Programme, Trienggadeng Sub-district, Pidie District	Ongoing
AmeriCares Foundation		
<i>HEAL 68 IN</i>	Dinas Kesehatan Provinsi Nangroe Aceh Darussalam - UPTD. Laboratorium Kesehatan	Design
<i>HEAL 70 IN</i>	Puskesmas Rehabilitation	Design
<i>HEAL 69 IN</i>	SHC Development	Design
American Red Cross		
<i>HEAL 126 IN</i>	AMERICAN RED CROSS-Integrated Community Health, Hygiene and Nutrition Education Pilot Project	Ongoing
<i>INST 38 IN</i>	AMERICAN RED CROSS-Integrated Community Based Risk Reduction Project (in cooperation with the Red Cross Movement partners)	Ongoing
Architectes de l'urgence		
<i>INFRA 32 IN</i>	Reconstruction of T.P.I. Pasi Pekan Baro	Design
<i>INFRA 33 IN</i>	Road Reconstruction, Pasi Rawa to Pasi Pekan Baro.	Completed
Asian Development Bank		
<i>ECON 95 Multi</i>	Replanting and Intensification of old coconut holdings with intercropping with food crops in Aceh Besar.txt	Design
<i>INFRA 77 Bilat</i>	Canadian Support to Community Water Services and Health (CSCWASH) – includes C\$ 5 million grant to the ADB Community Water Services and Health Aceh/Nias-North Sumatra Project, and C\$ 1.7 million for TA and Monitoring	Design
<i>ECON 107 Bilat</i>	Overall ADB project: Earthquake and Tsunami Emergency Support Project (ETESP) Sectors: Productive, Financial Subproject: Livelihood and Microfinance Support	Design
Astra Honda Motor		
<i>ECON 124 LN</i>	Tempat Pelelangan Ikan (TPI), Ulee Lheue, Banda Aceh	Design
<i>HEAL 105 LN</i>	Puskesmas, Lampulo, Kuta Alam, Banda Aceh	Design
Austcare		
<i>ECON 9 IN</i>	Lam Bada Lhok Community Livelihoods	Ongoing
<i>Econ 112 IN</i>	Aceh Besar Community Livelihoods Brick Production Project	Design
<i>ECON 10 IN</i>	Secondary Crop Farming in Pidie District	Ongoing
Australian Red Cross		
<i>INFRA 214 IN</i>	Permanent Housing Project - Aceh Besar (CPR90)	Ongoing
BAPPENAS		
<i>INFRA 95 Bilat</i>	Rehabilitation and Reconstruction of West Coast Road in North Sumatra	Ongoing
<i>INST 1 Bilat</i>	Training for Sub-districts officers of the province of NAD in Development Planning	Design
<i>INST 9 Bilat</i>	Public Consultation of R3MAS	Design
BGR/GTZ		
<i>SPAT 5 Bilat</i>	Management of Geo-Hazards	Design
BRR		
<i>INFRA 34 Multi</i>	Earthquake and Tsunami Emergency Support Project (ETESP) – HOUSING component	Design
<i>INST 19 IN</i>	Aceh Technical Assistance Recovery Project	Design
Badan Pertanahan Nasional		
<i>INFRA 215 IG</i>	SUPPORT TO THE RECONSTRUCTION OF THE ACEH LAND ADMINISTRATION SYSTEM”	Ongoing
Belgian Red Cross Fr		
<i>Econ 113 IN</i>	Projet de rehabilitation Marine en Aceh	Design
Bupati Aceh Besar		
<i>CROSS 3 IN</i>	Reconstruction of Gurah Village	Ongoing
<i>CROSS 5 IN</i>	Reconstruction of the village Lam Lumpu	Ongoing
<i>CROSS 4 IN</i>	Reconstruction of the Villages of Lampuyang, Palo, and Blang Situngkoh on Pulo Aceh	Ongoing
CAM		
<i>HEAL 20 IN</i>	Primary and Secondary Health Care and Water and Sanitation Assistance to Tsunami-Affected Areas in East and West Aceh Province, Sumatera (Bireuen, Pidie and Aceh Jaya) This project will be completed by a psychosocial project in the same areas	Ongoing
CARDI NRC		
<i>SOCI 26 IN</i>	Distribution of non-food items	Design
<i>EDUC 52 IN</i>	Education in emergencies	Design
<i>EDUC 50 IN</i>	Reconstruction and rehabilitation of Schools in tsunami affected areas, Aceh Barat	Ongoing
<i>INFRA 73 IN</i>	House reconstruction and rehabilitation in Tanjung Deah Village	Ongoing
<i>INFRA 74 IN</i>	Reconstruction of 41 concrete 2-floors-buildings (Ruko) for traders and their families in Meulaboh	Ongoing
<i>INFRA 142 IN</i>	Shelter Construction and Rehabilitation in Lancang Paru Village, Bandar Baru, Pidie	Ongoing
CARE		
<i>INFRA 8 Bilat</i>	GTZ/CARE International Pilot House Project	Completed

RAN Database Summary Report

Partner / Project ID	Title	Project Status
CARE International Indonesia		
HEAL 51 IN	Integrated Health, Hygiene and Sanitation for IDP Communities in Aceh	Design
CARITAS SWITZERLAND		
INFRA 154 IN	Deep Borehole Drilling for Drinking Water Supply in Meulaboh	Approval
INFRA 161 IN	Rekonstruksi Rumah di Aceh Barat dan Singkil	Design
Cross – 0017 - IN	Cross – 0017 - IN	Ongoing
CCP		
HEAL 38 IN	The ACEH Project: Advocacy, Communication, and Education for Health	Ongoing
CHF International		
ECON 43 IN	Lampulo Market Reconstruction	Design
CIDA		
CROSS 8 IN	Program	Initial Phase
CRS		
CROSS 1 IN	CRS Aceh Community-Based Recovery And Development, "ACCORD"	Design
HEAL 16 IN	Womens & Childrens Hospital, Banda Aceh	Ongoing
INFRA 27 IN	Water and Sanitation system in Lam Sujen and Krung Kala, Lhoong sub district	Completed
SPAT 1 IN	City Park Restoration, Banda Aceh	Ongoing
INFRA 194 IN	INFRA 194 IN (batch 10) Provision of 415 units of Permanent House in Aceh Selatan District	Ongoing
INFRA 195 IN	INFRA 195 IN (batch 10) Provision of 374 units of Permanent House in Nagan Raya District	Ongoing
INFRA 199 IN	INFRA 199 IN (Batch 10) Lamno Calang Road Repair and Urgent Small Works Program	Ongoing
CROSS 2 IN	Reconstruction of the Village of Mon Ikun	Ongoing
CWS		
INFRA 114 IN	BUILD A VILLAGE IN NIAS EMERGENCY AND RECOVERY PROGRAM – CWS INDONESIA	Ongoing
Caritas Czech Republic		
EDUC 49 IN	MAN 2	Ongoing
Center for Research and Community Development		
ECON 51 IN	Chili Planting	Ongoing
Children of Sumatera		
INFRA 113 IN	Watsan, and to provide healthcare as well as general welfare for children and their families affected by the Tsunami, and the resulting damage, on the island of Pulua Weh	Design
Children on the Edge		
SOCI 5 IN	Neuheun Child and Community Centre	Ongoing
Christian Children's Fund		
SOCI 23 IN	Recovery and Restoration Program	Completed
Cis Council		
Infra – 0147 - LN	Infra – 0147 - LN	Ongoing
Coastal Resources Center(University of Rhode Island)		
EDUC 24 IN	"Strengthening the University Role in Aceh Recovery and Reconstruction"	Design
Concern Worldwide		
EDUC 17 IN	Aceh Besar - Education Material Re-Supply	Design
EDUC 19 IN	Pulau Nasi – School & Community Buildings Reconstruction	Ongoing
INFRA 28 IN	Pulau Nasi – Infrastructure Reconstruction	Ongoing
INFRA 30 IN	Environmental Health Watsan	Ongoing
CROSS 6 IN	Concern Simeulue Rehabilitation & Reconstruction Programme	Ongoing
Concern for Kids		
ECON 98 IN	Krueng Sabee Livelihood Kits	Ongoing
INFRA - 0177 - IN	Krueng Sabee Raised Platforms for Tent Floors	Ongoing
Conservation International		
ECON 48 IN	Sustain Sumatra Alliance – Aceh Livelihood and Land Use Rehabilitation Program	Ongoing
Counterpart International		
ECON 48 IN	Sustain Sumatra Alliance – Aceh Livelihood and Land Use Rehabilitation Program	Ongoing
DAI (Development Alternatives Incorporated)		
ECON 104 IN	Support for Peaceful Democratization (SPD), Community-Based Recovery (CBR) Initiative and Small Grants Program	Design
DANIDA		
INFRA 205 IN	INFRA 205 IN (Batch 10)	Ongoing
DEA		
ECON 119 IN	Pemberdayaan ekonomi masyarakat korban Tsunami di NAD	Design
DLA Piper-Rudnick		
ECON 44 IN	village.	Ongoing
INFRA 64 IN	Grant Agreement with Dailami Nyak for Reconstruction/re-equipping of the Labui Boat Building Works	Completed
Departement of Public Works		
INFRA 80 IN	Community Shelter Reconstruction Project	Design
Dinas Pekerjaan Umum		
INST 37 IG	Support to shelter coordination in Nanggroe Aceh Darussalam"	Ongoing

RAN Database Summary Report

Partner / Project ID	Title	Project Status
Dinas Perindustrian dan Perdagangan Aceh Besar		
<i>ECON 168 IG</i>	Supporting Recovery of Small Industrial and Trades in Aceh Besar	Ongoing
Dinas Perindustrian dan Perdagangan Banda Aceh		
<i>ECON 167 IG</i>	Supporting Recovery of Small Industries and Trades in Banda Aceh	Ongoing
Dinas Sumber Daya Air		
<i>ECON 6 Multi</i>	Overall Asian Development Bank Project: Earthquake and Tsunami Emergency Support Project (ETESP)	Design
Diponegoro University – Semarang		
<i>INST 2 Bilat</i>	Training in Sustainable Coastal Development	Design
Education International		
<i>EDUC 101 IN</i>	Computer Skills Training	Design
Enfants Refugees du Monde (ERM)		
<i>SOCI 15 IN</i>	Educative and psychosocial support for children & their families affected by the Tsunami	Ongoing
<i>EDUC 77 IN</i>	Educative and psychosocial support for children & their families affected by the Tsunami in the Province of Aceh	Ongoing
FIG-Indonesia		
<i>INFRA 79 LN</i>	Pembangunan rumah-rumah	Design
FIG-Indonesia		
<i>ECON 57 LN</i>	Pembuatan dan perbaikan perahu nelayan	Ongoing
<i>EDUC 58 LN</i>	Pembangunan sekolah-sekolah	Design
<i>INFRA 83 LN</i>	Perbaikan pompa air	Design
Farnow		
<i>INFRA 105 IN</i>	Kota Kuning Hijai - Bireuen	Design
Fauna and Flora International (FFI)		
<i>ECON 131 IN</i>	Community-based integrated mangrove rehabilitation and economic recovery program in Tsunami effected villages in Pulau Weh, Aceh	Design
<i>ECON 132 IN</i>	Sustainable livelihoods and Landuse planning Aceh Jaya district – Jaya and Sampoinit	Design
<i>ECON 133 IN</i>	Sustainable livelihoods and Landuse planning Aceh Jaya district - Panga and Krueng Sabee	Design
<i>ECON 134 IN</i>	Sustainable livelihoods and Landuse planning Aceh Jaya district – Teunom and Setia Bakti	Design
Food Agriculture Organization (FAO)		
<i>ECON 64 UN</i>	Assistance for Small Scale Fish Processing in Aceh Besar	Design
<i>ECON 7 IN</i>	Rehabilitation of the agricultural means in the tsunami affected area	Ongoing
<i>ECON 129 UN</i>	REHABILITATION OF LIVELIHOODS IN THE FISHERIES SECTOR AFFECTED BY THE TSUNAMI AND THE EARTHQUAKE IN INDONESIA	Design
<i>ECON 130 UN</i>	Emergency in-kind assistance to fisheries communities in Indonesia	Design
<i>ECON 157 UN</i>	ECON 157 UN (BATCH 10) - Livestock Production and Health	Ongoing
<i>ECON 159 UN</i>	ECON 159 UN (BATCH 10) - Support to farmers in tsunami-affected areas through the provision of agricultural and livestock inputs.	Ongoing
<i>ECON - 0148 - UN</i>	Assistance to tsunami-affected coastal communities in Aceh and North Sumatra, INCLUDING Nias Island, Indonesia.	Ongoing
Food for the Hungry International (FHI)		
<i>EDUC 62 IN</i>	English Program	Design
<i>INFRA 104 IN</i>	Bukit Soeharto Water Project	Design
<i>INFRA 81 IN</i>	Meulaboh Central Drainage Canal	Design
<i>EDUC 78 IN</i>	English Education Program	Design
<i>EDUC 82 IN</i>	FHI's Educational and English training for Johan Pahlawan, Aceh Barat	Design
ForesTrade		
<i>ECON 48 IN</i>	Sustain Sumatra Alliance – Aceh Livelihood and Land Use Rehabilitation Program	Ongoing
Forum LSM Aceh		
<i>INST - 0032 - LN</i>	programme is a training and monitoring project focusing on various organs of the government in Aceh province. It will focus on a provincial level, and in Banda Aceh, Aceh Besar	Ongoing
French Embassy		
<i>EDUC 21 IN</i>	Schools - Reconstruction & Rehabilitation	Design
<i>EDUC 3 Bilat</i>	13 Schools reconstruction and rehabilitation	Design
<i>INFRA 12 IN</i>	Permanent houses reconstruction program and economic recovery for fishermen communities in Kec. Simpang Tiga, Kab. Pidie	Ongoing
French Red Cross		
<i>ECON 85 IN</i>	Market Rehabilitation	Design

RAN Database Summary Report

Partner / Project ID	Title	Project Status
GTZ		
<i>ECON 71 Bilat</i>	Microfinance	Ongoing
<i>ECON 8 Bilat</i>	Neuheun Brick Factory Repair/Reconstruction	Design
<i>EDUC 5 Bilat</i>	Tibang School Project	Design
<i>INFRA 6 Bilat</i>	GTZ/AMURT Neuheun House Reconstruction Project	Ongoing
<i>INFRA 7 Bilat</i>	GTZ/AMURT Neuheun House Repair Project	Ongoing
<i>INFRA 8 Bilat</i>	GTZ/CARE International Pilot House Project	Completed
<i>INST 10 Bilat</i>	Reconstruction and Development of Population Administration Services in NAD	Ongoing
<i>INST 11 Bilat</i>	Support to Local Governments and Community Planning	Design
<i>SPAT 3 Bilat</i>	Spatial and Environmental Planning and Management	Design
GTZ KfW		
<i>EDUC 60 Bilat</i>	Rehabilitation and Reconstruction of Vocational Training Centres	Design
<i>HEAL 45 Bilat</i>	Rehabilitation and Reconstruction of Provincial and District Health Systems (Joint FC/TC)	Ongoing
<i>HEAL 46 Bilat</i>	Rehabilitation and Reconstruction of Zainoel Abidin Hospital Banda Aceh (Joint FC/TC)	Design
<i>INFRA 84 Bilat</i>	Rehabilitation and Reconstruction of Housing and Human Settlements	Design
<i>EDUC 70 Bilat</i>	Rehabilitation and Reconstruction of Secondary Schools	Design
GenAssist		
<i>ECON 30 IN</i>	Chili Planting	Ongoing
<i>ECON 31 IN</i>	Repair shop	Design
<i>ECON 32 IN</i>	Build 17 Becaks	Design
<i>ECON 33 IN</i>	Doy River Cleaning	Design
<i>INFRA 47 IN</i>	Genset	Design
<i>INFRA 48 IN</i>	Housing	Design
<i>INFRA 49 IN</i>	Mukim Warehouse	Design
<i>EDUC 40 IN</i>	School Kits	Completed
<i>INFRA 127 IN</i>	Permanent Shelter in Blang Mee Mukim, Lhoong Sub-District, Aceh	Initial Phase
<i>ECON 29 IN</i>	Soil testing	Ongoing
German Agro Action (GAA)		
<i>INFRA 100 IN</i>	Semi Permanent shelter construction and shelter assistance for the tsunami and earthquake victims of Simeulue Island, Aceh, Indonesia	Design
<i>INFRA 148 IN</i>	Water rehabilitation for the tsunami victims in Pidie and Bireuen, Aceh province	Completed
<i>INFRA 133 IN</i>	Indonesia	Ongoing
<i>INFRA 134 IN</i>	Supporting the recovery of shelter and livelihoods in Tsunami affected villages in the districts of Pidie and Bireuen	Design
<i>EDUC 111 IN</i>	EDUC 111 IN (BATCH 10) - Re-construction of 5 schools in Aceh Jaya Region, NAD Province, Indonesia	Ongoing
<i>INFRA 204 IN</i>	INFRA 204 (Batch 10) - Supporting the recovery of shelter and livelihoods in Pantaraja village in the districts of Pidie and Bireuen	Ongoing
Gong Pasee		
<i>INFRA 91 IN</i>	Housing Development Project for Tsunami, Victims in Meunasah Sagoe Village	Completed
Grameen Foundation USA		
<i>ECON 115 IN</i>	Tsunami Micro Finance Initiative. It will introduce Micro Finance to the Tsunami affected peoples of Aceh province	Ongoing
Gruppo Volontariato Civile (GVC)		
<i>SOCI 27 IN</i>	After tsunami: starting back from children	Ongoing
<i>INFRA 78 IN</i>	Going back home	Ongoing
<i>EDUC-87-IN</i>	EDUC-87-IN (batch 7) Going back school	Ongoing
Habitat for Humanity Indonesia		
<i>INFRA 101 IN</i>	Tsunami Disaster Response Project	Ongoing
<i>INFRA 217 IN</i>	Housing Construction in	Ongoing
Handicap International		
<i>HEAL 71 IN</i>	Disability Program for Aceh Province	Design
Helen Keller International		
<i>HEAL 73 IN</i>	Primary Eye Care (PEC) Program	Design
<i>HEAL 74 IN</i>	Supplementation with Vitamins and Minerals (SUM)	Ongoing
Help		
<i>INFRA 156 IN</i>	Reconstruction and Rehabilitation of the village Kuala Keureutou, District Lhokseumawe, Sumatra - Housing	Design
<i>ECON 111 IN</i>	Sumatra	Design
<i>INFRA 128 IN</i>	Reconstruction and Rehabilitation of the village Kuala Keureutou, District Lhokseumawe, Sumatra	Ongoing
<i>INFRA 130 IN</i>	Reconstruction and Rehabilitation of the village Kuala Keureutou, District Lhokseumawe, Sumatra	Ongoing
<i>INFRA 131 IN</i>	Construction temporary market	Ongoing
<i>ECON 137 IN</i>	Mangrove and terrestrial nursery project in vilage Tibang, Syiah Kuala – Banda Aceh, Aceh Besar, Sumatra	Design

CAUTION : First Data Collection Round.
Validation in progress.

RAN Database Summary Report

Partner / Project ID	Title	Project Status
Hilfswerk Austria		
INFRA 135 IN	district	Ongoing
SOCI 33 IN	Anak Cacat Banda Aceh – jangan lupa kami	Design
HEAL 76 IN	Meuraxa Hospital	Design
Hope International		
INFRA 45 IN	Reconstruction & Rehabilitation Buildings, at Dept of Agriculture Dinas Perkebunan	Ongoing
EDUC 38 IN	Universitas Muhammadiyah Aceh, Rehabilitation and reconstruction	Design
EDUC 39 IN	Building Rehabilitation/ Construction at SMP17 school in Ulee Lheue , Banda Aceh	Completed
HEAL 21 IN	HOPE Indonesia (Hospital Preparedness for Emergencies	Ongoing
IACO		
EDUC 16 IN	Rehabilitation of Schools In Aceh	Completed
INFRA 25 IN	Reconstruction of Batee Bridge, Pasir Gentang, Pidie	Completed
INFRA 26 IN	Engineering Analysis of Infrastructure on Simeulue	Completed
IAIN AR-RANIRY – The State Institute for Islamic Studies – Banda Aceh		
EDUC 57 IN	IAIN-Indonesia Social Equity Project (IISEP)	Design
SOCI 52 IN	SOCI – 0052 – IN (Batch 10) - IAIN AR-RANIRY – The State Institute for Islamic Studies – Banda Aceh	Ongoing
ICMC		
SOCI 30 IN	Care and Support for Extremely Vulnerable Individuals	Design
SOCI 31 IN	Psycho-social support and Trauma Recovery Program	Ongoing
ECON 138 IN	Income generation activities	Ongoing
IDES		
HEAL 42 IN	Support to the provincial health system for the medicines and medical supply management in Aceh Province	Ongoing
HEAL 83 IN	Support to the provincial health system for the medicines and medical supply management in Aceh Province	Design
INFRA 189 IN	INFRA 189 IN (batch 10) (Shelter assistance for Teunom, Aceh Jaya)	Ongoing
IFC		
ECON 139 Multi	PEP-Aceh/Nias	Design
IMC		
HEAL 17 IN	Rehabilitation and support of clinics in Nias, North Sumatra	Design
HEAL 18 IN	Rehabilitation and support of Gunungsitoli Hospital, Nias, North Sumatra	Design
IRC		
INFRA 11 IN	Environmental Health Interventions for survivors of the December 2004 Tsunami and the March Nias earthquake.	Ongoing
SOCI 1 IN	Child and Youth Development and Protection for survivors of the December 2004 Tsunami and March Nias Earthquake	Ongoing
HEAL 92 IN	(BATCH7) HEAL-92-IN Health Service Delivery, Public and Reproductive Health Interventions for survivors of the December 2004 Tsunami and the March Nias earthquake	Ongoing
ECON 12 IN	Community Regeneration Program	Ongoing
IRM NAD (Ikatan Remaja Muhammadiyah Nanggroe Aceh Darussalam)		
ECON 68 UN	Farmers' Fish Pond Rehabilitation in Pidie	Design
ITB		
ECON 99 Bilat	Local Economic & Resources Development Training Program for Aceh	Design
Indonesian International Education Foundation (IIEF)		
EDUC 22 IN	Rebuilding Higher Education in Aceh	Design
International AID		
HEAL 81 IN	Community Base Health Program, Lolofitu Moi Subdistrict, District of Nias, N.Sumatra	Design
HEAL 80 IN	Aceh Medical Equipment Service Center (AMESC) Sector: Health Partner: DINKESLocation: based in Banda Aceh with a coverage area of the whole province of Aceh	Design
International Labour Organization (ILO)		
ECON 53 Bilat	CIDA Support to ILO - Entrepreneurship Culture and Business Creation for youth Employment in Aceh	Initial Phase
ECON 79 UN	ILO Aceh Programme on Employment Services	Ongoing
ECON 80 UN	ILO Aceh Programme on Skills Development Filling Skills Gaps through Vocational Training	Ongoing
ECON 81 UN	ILO Aceh Programme Support Micro enterprise and Self	Ongoing
ECON 82 UN	ILO Aceh programme Labour Based Infrastructure Rehabilitation and Reconstruction	Ongoing
ECON 83 UN	ILO Aceh Programme Prevention of Child Labour providing youth with life skills	Ongoing
ECON 84 UN	ILO Aceh Programme Local Economic Recovery and Development Rebuilding Livelihoods and Employment Opportunities	Design

RAN Database Summary Report

Partner / Project ID	Title	Project Status
International Organization for Migration (IOM)		
<i>SOCI 24 IN</i>	Empowering Vulnerable Communities in Need to Prevent Trafficking in People in Aceh	Ongoing
<i>INFRA 69 IN</i>	Improving Water & Sanitation Conditions of Acehese Displaced by the Earthquake & Tsunami in Indonesia	Ongoing
<i>INFRA 70 IN</i>	Rehabilitation and Capacity Building of Primary Health Care Centres Damaged by the Earthquake & Tsunami in Indonesia	Ongoing
<i>INST 22 IG</i>	2)	Design
<i>INST 16 IG</i>	International Organization for Migration (IOM)	Design
<i>ECON 100 IG</i>	Immediate Emergency Relief in Nias and Simeulue Islands in Indonesia	Design
<i>INFRA 139 IG</i>	Transitional Housing In Nanggroe Aceh Darussalam	Design
<i>INFRA 108 IG</i>	Transitional Housing In Nanggroe Aceh Darussalam	Design
<i>INST 18 IG</i>	International Organization for Migration (IOM)	Design
<i>INST 21 IG</i>	Three Days Seminar Games On Human Rights And Introduction On Community Policing For Police Officers In Polda Nanggroe Aceh Darussalam	Design
International Relief and Development (IRD)		
<i>HEAL 78 IN</i>	Health Grants Management Program in Aceh (Phase II)	Design
Islamic Relief		
<i>EDUC 69 IN</i>	Reconstruction of SDN1 Lhok Nga	Design
<i>ECON 153 IN</i>	IDRF-funded Livelihood Program - Islamic Relief	Ongoing
<i>EDUC 109 IN</i>	EDUC 109 IN (BATCH 10) - IDRF-Funded School Rehabilitation	Ongoing
<i>INFRA 211 IN</i>	Construction of Earthquake Resistant Homes	Ongoing
Italian Cooperation		
<i>HEAL 88 Bilat</i>	Sub-district Peukan Bada: Reconstruction of 1 Puskesmas, 1 Postu, 6 Polindes	Ongoing
<i>ECON 116 Bilat</i>	To Construct a Cold Storage of 400m2, in the harbour of Peudada in Samalanga Sub-district, Bireuen District, and to provide a freezer truck for transport of products	Ongoing
<i>CROSS – 0015 - BILAT</i>	Emergency Program to Support the Indonesian People Tsunami strike.	Ongoing
JARKAS		
<i>INFRA - 0182 - Bilat</i>	Aceh Besar, Kecamatan Lhoknga	Ongoing
JICA		
<i>SOCI 29 Bilat</i>	Rehabilitation and Reconstruction Orphanages	Design
<i>EDUC 55 IN</i>	Restoration and Enhancement of Unsyiah Academic and Research Capacity	Design
<i>INFRA 107 Bilat</i>	Rehabilitation and Economic Empowerment and Sanitation Development for Refugees of Tsunami Victims in Kemukimam Lampageu, Peukan Bada Subdistric, Aceh Besar Dist	Design
<i>SPAT 4 Bilat</i>	(URRP)	Design
<i>ECON 156 Bilat</i>	ECON 156 Bilat (BATCH 10) - Supporting Program for the Fishery Community by Providing Motorboat and Training the Community for Productivity Improvement in Afulu and Lahew Sub-district, Nias District North Sumatra Province	Ongoing
<i>SOCI 54 BILAT</i>	SOCI 54 BILAT (BATCH 10) - Community –based Psychosocial Recovery Program Focusing on Women Living in IDP Camps	Ongoing
<i>SOCI 55 Bilat</i>	SOCI 55 Bilat (Batch 10) - Community –based Psychosocial Recovery Program Focusing on Women Living in IDP Camps	Ongoing
JICS		
<i>ECON 72 Bilat</i>	Rehabilitation of Local Markets	Design
<i>ECON 73 Bilat</i>	Support for Vocational Training	Design
<i>ECON 91 Bilat</i>	Rehabilitation of people community after earthquake and Tsunami in Kec. Peukan Bada	Design
<i>EDUC 65 Bilat</i>	Support for Madrasah Pesantren and public schools	Design
<i>EDUC 66 Bilat</i>	Support for Universities	Design
<i>HEAL 52 Bilat</i>	Supply of Medicine	Design
<i>HEAL 53 Bilat</i>	To rebuild and rehabilitate health centers	Design
<i>INFRA 96 Bilat</i>	Selected Emergency Repair Work of Flood Way Dyke in Banda Aceh	Design
<i>INST 12 Bilat</i>	Land Document Recovery	Ongoing
Japanese Red Cross		
<i>INFRA 216 IN</i>	Construction of Permanent Housing in Aceh Barat District	Ongoing

RAN Database Summary Report

Partner / Project ID	Title	Project Status
Jaringan Kasih (JARKAS)		
<i>ECON 3 Multi</i>	Overall Asian Development Bank project: Earthquake and Tsunami Emergency Support Project (ETESP)	Design
<i>ECON 4 Multi</i>	Overall Asian Development Bank project: Earthquake and Tsunami Emergency Support Project (ETESP)	Design
<i>ECON 40 IN</i>	Economic Revitalization in Pidie District.	Design
<i>ECON 41 IN</i>	Aceh.	Design
<i>ECON 42 IN</i>	Grant Agreement with Panglima Laot for the Rehabilitation of the Lamnyong Market.	Design
<i>ECON 45 IN</i>	Grant agreement for the provision of financial assistance to ASEPHI for the rehabilitation of the traditional handicrafts in Aceh Province.	Ongoing
<i>ECON 47 IN</i>	Aceh Recovery and Reconstruction Program	Ongoing
<i>ECON 49 GI</i>	RIGP (Livelihood Recovery of Community Affected by Earthquake and Tsunami in Province NAD and North Sumatera)	Ongoing
<i>ECON 5 Multi</i>	Overall Asian Development Bank Project: Earthquake and Tsunami Emergency Support Project (ETESP)	Design
<i>ECON 52 IN</i>	Community Development Program	Ongoing
<i>ECON 65 UN</i>	Assistance for Temporary Fish Landing Facility in Ulelhee, Aceh Besar	Ongoing
<i>ECON 66 UN</i>	Assistance for Small Scale Fish Processing in Bireun and Aceh Utara	Ongoing
<i>ECON 93 Multi</i>	Earthquake & Tsunami emergency Support Project (ETESP) Agriculture Component	Design
<i>ECON 94 Multi</i>	Replanting and Intensification of old coconut holdings with intercropping with food crops in Bireun.	Design
<i>EDUC 6 Bilat</i>	Australia Indonesia Partnership for Reconstruction and Development: Aceh Rehabilitation Program: Education Sector Assistance	Design
<i>HEAL 28 IN</i>	Medic Psychosocial for Krueng raya	Design
<i>HEAL 39 IN</i>	Provision of Computer Equipment to the Provincial Dept. of Health, NAD.	Design
<i>INFRA 103 LN</i>	School and House Reconstruction	Design
<i>INFRA 31 IN</i>	Housing - Reconstruction	Ongoing
<i>INFRA 56 IN</i>	Shelter and Wat/San project in Nagan Raya	Design
<i>INFRA 62 IN</i>	Grant Agreement with Badan Metereologi dan Geofiska Department (BMG) of Banda Aceh for the provision of basic operating equipment.	Completed
<i>INFRA 71 IN</i>	DISASTER RESPONSE LOGISTICS	Ongoing
<i>INFRA 75 IN</i>	Land Clearing	Design
<i>INFRA 85 IN</i>	Waste Management Banda Aceh	Initial Phase
<i>INFRA 86 Bilat</i>	Provision of Communal Water and Sanitation Facilities for the Tsunami Victims in Neuheun	Ongoing
<i>INFRA 87 IN</i>	Kota Kuning Hijai – Lhoknga	Initial Phase
<i>INFRA 88 IN</i>	Kota Kuning Hijai – Pulau Nasi	Initial Phase
<i>INFRA 90 IN</i>	Reconstruction of 95 houses, Angkeo, Simeulue	Ongoing
<i>INFRA 92 IN</i>	Water Project Blang Krueng	Ongoing
<i>INFRA 94 Bilat</i>	Sanitatin and Park Department, Banda Aceh Municipality	Ongoing
<i>INFRA 97 Bilat</i>	Water supply and sanitation	Ongoing
<i>INST 13 Bilat</i>	Support for RadioTV Broadcasting Activities	Design
<i>SPAT 2 IN</i>	mapping	Design
<i>ECON 123 IN</i>	Green Coast Recovery Project, Securing the Future of Nature and People after the Tsunami	Design
<i>SOCI 32 IN</i>	Mobile Child Care	Ongoing
<i>INFRA 109 IN</i>	Nias Emergency And Recovery Program – Cws Indonesia	Design
<i>HEAL 74 IN</i>	Supplementation with Vitamins and Minerals (SUM)	Ongoing
<i>INFRA 141 Bilat</i>	AIPRD Interim Governance Programme	Initial Phase
<i>HEAL 87 IN</i>	kerja bakti - bintang kecil-bekerjasama dengan siswa dan ibu rumah tangga meningkatkan kesadaran masyarakat Krueng raya akan mewujudkan masyarakat krueng raya yang sehat dan bertanggung jawab terhadap lingkungan	Design
<i>INFRA 162 IN</i>	Housing Construction project in Seubun Ketapang Village, Lhoknga, Aceh Besar	Ongoing
<i>INFRA 197 IN</i>	INFRA 197 IN (Batch 10) ZOTF Sirombu Village community reconstruction project.	Ongoing
<i>HEAL - 0108 - IN</i>	Room of the Permanta Hati Hospital; Equipping the Emergency Room of the BLPKM Hospital; Equipping the Permanta Hati Hospital; Equipping Nurbarhari Clinic; Equipping four D	Ongoing
<i>INFRA - 0180 - IN</i>	Proyek Pembangunan Perumahan Cinta Kasih Tzu chi di Nanggroe Aceh Darussalam	Ongoing
<i>INFRA - 0181 - Bilat</i>	Rehabilitation of the Water Treatment Plant Lambaro	Ongoing
<i>SOCI - 0050 - IN</i>	Teaching of Acehese Traditional Art as Alternative Trauma Treatment for Internally Displaced Children and Villages of Kota Banda Aceh, Greater Ace Regency, Pidie regency, and Bireuen Regecy	Ongoing
<i>EDUC-89-IN</i>	EDUC-89-IN (Batch 7) Reconstruction of Schools by DIS	Ongoing
<i>INFRA 218 IN</i>	Australian Red Cross - Reconstruction in Nias Island	Ongoing
<i>INFRA 212 IN</i>	Simeulue Island Community Based Construction (CPR52)	Ongoing
<i>INFRA 213 IN</i>	Simeulue Island Reconstruction - Sinabang City Housing (CPR53)	Ongoing
(JUH)		
<i>HEAL -91-IN</i>	(BATCH7) HEAL -91-IN (First Aid Training (Latihan Pertolongan Pertama))	Ongoing

*CAUTION: First Data Collection Round.
Validation in progress.*

RAN Database Summary Report

Partner / Project ID	Title	Project Status
KOICA		
<i>INFRA 171 Bilat</i>	Provision of equipment for the reconstruction work such as heavy equipment and donation of vessels	Design
<i>ECON 140 Bilat</i>	Rehabilitation of Mangrove Forest damaged by Tsunami	Design
<i>EDUC 103 Bilat</i>	Construction of Primary School in Aceh Besar and Aceh Jaya	Design
<i>HEAL 93 Bilat</i>	The Reconstruction of Health Sector – Construction of Hospitals and Provision of Medical Equipments	Design
<i>INST 25 Bilat</i>	Invitation of trainees	Design
KOTIB NAD-SUMUT/ Dina Kartika Sari		
<i>SOCI 39 IN</i>	Support Programme for the Tsunami Victims in Aceh and Nias	Ongoing
Keio University		
<i>EDUC 80 Bilat</i>	SOI Asia Unsyiah	Design
Kolaborasi Nurani		
<i>ECON – 0141 – LN</i>	ECON – 0141 – LN (Batch 8) Development & Construction of “PASAR ACEH” Complex, in the city of	Ongoing
Komisi Independen Pemilu (KIP)		
<i>ECON 46 IN</i>	Penayong Market Reconstruction	Design
<i>ECON 50 GI</i>	Rehabilitation of Tsunami Affected Agricultural Areas in Nanggroe Aceh Darussalam Province	Design
<i>ECON 58 UN</i>	Fishing Capacity Recovery – Layeun, Leupung A.Besar District,	Design
<i>ECON 74 UN</i>	Livelihood Recovery in Pidie District , Simpang Tiga, Jangka Buya, Kembang Tanjong, Batee, Panter	Ongoing
<i>EDUC 43 IN</i>	Kindergarten	Design
<i>EDUC 45 IN</i>	School Reconstruction – Sekolah Dasar (SD) Deah Rungkom, Kec. Baitussalam, Aceh Besar	Design
<i>EDUC 47 IN</i>	School Reconstruction – Sekolah Dasar (SD) Lam Gue-ue, Kec. Peukan Bada, Aceh Besar	Design
<i>EDUC 48 IN</i>	School Reconstruction – Sekolah Dasar (SD) Lam Nga, Kec. Mesjid Raya, Aceh Besar	Design
<i>INFRA 5 IN</i>	Emergency response for the displaced populations, victim of the tsunami and earthquake	Design
<i>EDUC 2 Bilat</i>	Twinning and sponsoring of schools in the area affected by tsunami in Sumatra	Ongoing
<i>EDUC 51 IN</i>	Reconstruction and rehabilitation of Schools in tsunami affected areas, Sigli-Pidie	Design
<i>EDUC 67 Bilat</i>	Rehabilitation of part of the SMKN2 Banda Aceh	Design
<i>HEAL 1 Bilat</i>	Twinning of Pediatric Departments of Zainal Abidin Hospital in Banda Aceh and Centre Hospitalo Universitaire of Lille (France)	Design
<i>HEAL 26 IN</i>	Public Health Project	Design
<i>HEAL 27 IN</i>	Revitalization of Puskesmas management and health services	Design
<i>HEAL 31 IN</i>	PUSKESMAS(II) – Jaya Baru	Design
<i>HEAL 35 IN</i>	Revitalisation of Sub-District and District Health Services Using Management Systems	Design
<i>HEAL 36 IN</i>	Strengthening community-based responses to traumatic stress	Design
<i>HEAL 37 IN</i>	Community Health Revitalization and Capacity Building in Aceh	Design
<i>HEAL 4 IN</i>	Health support to Tsunami / Earthquake affected population.	Design
<i>HEAL 40 IN</i>	Psychological Recovery Program in Aceh	Design
<i>SOCI 4 IN</i>	Mobile Care for children affected by Tsunami	Design
<i>INFRA 2 Multi</i>	Aceh Recovery and Reconstruction Community Broadcasting Information Services	Design
<i>INFRA 22 IN</i>	Meulaboh: Community Buildings	Design
<i>INFRA 29 IN</i>	Poulua Nasi – Shleter Reconstruction	Design
<i>INFRA 35 UN</i>	Emergency Water and Environmental Sanitation for Nanggroe Aceh Darussalam and North Sumatra Provinces	Design
<i>INFRA 55 Bilat</i>	Rehabilitation of Lambaro Water Treatment Plant	Design
<i>INFRA 57 IN</i>	Reconstruction and Community Recovery Program in Banda Aceh, Indonesia	Design
<i>INFRA 63 IN</i>	Grant Agreement with Zoe's Ark Foundation for resettlement housing for Mon Ikeun Village	Design
<i>INFRA 65 UN</i>	Lamno, Aceh Jaya Port Rehabilitation	Ongoing
<i>INFRA 66 UN</i>	Balohan Ferry Port Rehabilitation.	Ongoing
<i>INFRA 67 UN</i>	Ulee Lheu Port Rehabilitation.	Ongoing
<i>INFRA 68 IN</i>	Aceh Reconstruction/APS Indonesia 05-011	Design
<i>INFRA 72 LN</i>	Program Rekonstruksi Perkampungan dan Perekonomian Masyarakat Tepi Pantai Aceh	Design
<i>INFRA 9 Bilat</i>	RECONSTRUCTION	Design
<i>INST 4 IN</i>	Aceh Community Empowerment Program	Design
<i>INST 6 IN</i>	CAMP MANAGEMENT TRAINING, INFORMATION, COUNSELLING AND LEGAL ASSISTANCE	Design
<i>SOCI 11 IN</i>	Meulaboh: General Food Distribution	Design
<i>SOCI 12 IN</i>	Nias: General Food Distribution	Design
<i>SOCI 2 Bilat</i>	Aceh reconstruction and accessibility for the persons with disability to the new environment	Design
<i>INFRA 159 GI</i>	(NAD)	Design
<i>INST 26 UN</i>	Support to Strengthen the Capacity and Role of Civil Society Organizations in the Recovery of Communities in Aceh	Ongoing
<i>INFRA 149 Bilat</i>	Reconstruction Plan for Nanggroe Aceh Darussalam Province and Nias Island in North Sumatra Province	Design
<i>INST 23 IN</i>	Support for NGOs in the provinces of Aceh and North Sumatra	Ongoing
<i>INST 24 Multi</i>	Aceh Local Governance Action Programme	Design
<i>ECON 125 IN</i>	Savings Banks Reconstruction Fund for South Asia	Design

*CAUTION: First Data Collection Round.
Validation in progress.*

RAN Database Summary Report

Partner / Project ID	Title	Project Status
HEAL 100 IN	Tsunami Health Recovery Program in Nias	Design
HEAL 103 IN	Project ASRE 51: Emergency Response in Aceh Besar, Aceh Barat, Nagan Raya, Aceh Utara and Nias: Health Sector	Design
HEAL 104 LN	Project ASRE 51: Emergency Response in Aceh Besar, Aceh Utara, Aceh Barat and Nias for Tsunami and Earthquake: Psychosocial Sector	Design
INFRA 140 IN	Permanent houses reconstruction program and economic recovery in Kec. Simpang Tiga, Kab. Pidie	Design
INFRA 169 IN	Peukan Bada permanent housing reconstruction pilot project	Design
INFRA 198 UN	INFRA 198 UN (Batch 10) Port Development	Ongoing
ECON 24 LN	Brick Factory Project	Ongoing
SOCI 10 IN	Meulaboh: Child Friendly Activities	Ongoing
ECON – 0128 - LN	ECON – 0128 - LN (Batch 8) Micro enterprise development (MED) program	Ongoing
HEAL – 0100 - INT	(Batch 8)-HEAL – 0100 - INT sunami Health Recovery Program in Nias	Ongoing
HEAL - 101 - IN	(BACRH 8) HEAL - 101 - InRenovation of Lukas Public Hospital, Hillisimeatano, South Nias – This project will allow Lukas Hospital to function as a district hospital serving the area around Hillisimaetano and after completion of the new road Teluk Dalam	Ongoing
HEAL - 105 - LN	HEAL - 105 - LN (Batch 8) Puskesmas, Lampulo, Kuta Alam, Banda Aceh	Ongoing
INST - 27 - IN	Aceh Bangkit or "Renaissance of Aceh's Spirit" (Batch 8)	Ongoing
INFRA 169 IN	Peukan Bada permanent housing reconstruction pilot project	Ongoing
Komite Rehabilitasi dan Rekonstruksi Jambo Mesjid		
INFRA 160 IN	Village	Ongoing
LBH Anak		
SOCI 28 LN	Pendampingan Hukum bagi Perempuan dan Anak melalui lawyer dan community advocate	Design
Latter-day Saint Charities (LDSC)		
ECON 122 IN	AIRO – Fishing boat project	Design
HEAL 89 IN	NIAS-LUKAS Teluk Dalam Hospital Project	Design
HEAL 90 IN	Special Hospital Project-Zainoel Abidin General Hospital & Badan Pelayanan Kesehatan Jiwa	Design
HEAL 94 IN	KESDAM HOSPITAL – Rehabilitation Center Project	Design
ECON 149 IN	(Bireuen)	Ongoing
INFRA 178 IN	INFRA 178 IN (batch 10)(Homes & Community Buildings – Banda Aceh)	Ongoing
SOCI 53 LN	SOCI 53 LN (Batch 10) - PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
Leuser International Foundation		
ECON 92 IN	Aceh	Design
Local Empowerment Assistance Project Inc (LEAP)		
ECON 118 IN	Community Regeneration Through Small Industry Development	Design
Local Governance Support Program (LGSP)		
INST 17 LN	Local Governance Support Program / LGSP	Design
MSF CH		
HEAL 72 IN	Health support to Tsunami / Earthquake affected population	Design
MSF-Holland		
HEAL 65 Multi	West Coast Project (Aceh Barat)	Ongoing
HEAL 66 Multi	Takengon	Ongoing
HEAL 67 Multi	Lhokseumawe (North Coast)	Ongoing
Malteser International Lhokseumawe		
INFRA 152 IN	Village reconstruction and livelihood in Lancok and Jambo Timu	Ongoing
HEAL 95 IN	Equipment support Provincial Hospital	Design
HEAL 96 IN	Strengthening of Primary health care services for the Tsunami affected population in Nagan Raya District	Design
Medecins Du Monde		
HEAL 60 IN	Upgrading the capacity of health structures in the sub districts of Teupah Barat and Teluk Dalam in Simeulue Island, Aceh province, Indonesia	Ongoing
HEAL 7 IN	Aceh Jaya and Aceh Besar and support to the re-establishment of the Abidin hospital services	Ongoing
HEAL 75 IN	Reconstruction of Lhoknga puskesmas ,Doctors house , Nurse house and Support Facilities to provide health care access to the population	Ongoing
Medecins Sans Frontieres-Belgium		
HEAL 55 IN	Mental health programme Banda Aceh - Aceh Besar	Ongoing
HEAL 56 IN	Medical and mental health programme Lamno	Ongoing
HEAL 57 IN	Medical and mental health programme Sigli	Ongoing
Medecins Sans Frontieres-France		
HEAL 25 IN	Medical Assistance in Pidie District	Design
Medicos del Mundo		
HEAL 8 IN	RECONSTRUCTION OF CALANG PRIMARY HEALTH CARE CENTER AND RESTORATION OF PRIMARY HEALTH SYSTEM IN CALANG	Ongoing

RAN Database Summary Report

Partner / Project ID	Title	Project Status
Mennonite Central Committee		
<i>ECON 142 IN</i>	IN-13-03, 4, & 5: KYPA Fishing Equipment, Fish Processing Equipment, and a Children's Pavilion for Rheum Baroh	Design
<i>SOCI – 0037 – IN</i>	FK&P Trauma Healing, Banda Aceh & Nias	Ongoing
Mercy Corps		
<i>ECON 38 IN</i>	Livelihoods Revitalization	Design
<i>ECON 39 IN</i>	Financial Access Program (FinAP)	Design
<i>SOCI 25 IN</i>	Social Revitalization	Ongoing
<i>INFRA 60 IN</i>	Cash for Work (CfW)	Design
<i>INFRA 61 IN</i>	Support for Return and Village Recovery	Design
Mercy Malaysia		
<i>EDUC 42 IN</i>	SMU Lhoknga	Ongoing
<i>INFRA 53 IN</i>	Core House Desa Weu Raya	Ongoing
<i>EDUC 41 IN</i>	MTSN Lamhom - SCHOOL	Ongoing
<i>HEAL 29 IN</i>	Rehabilitation of Orthopedic Ward, RSU Zainal Abidin	Ongoing
<i>HEAL 30 IN</i>	PUSKESMAS Panga	Ongoing
<i>HEAL 32 IN</i>	Akademik Farmasi (AKFAR) Dinas Kesehatan	Ongoing
<i>HEAL 33 IN</i>	Akademi Perawat (AKPER) Departemen kesehatan (DEPKES)	Ongoing
<i>HEAL 34 IN</i>	Akademi Perawat (AKPER) Dinas Kesehatan	Ongoing
<i>INFRA 54 IN</i>	Relocation House Sebulun Ayun	Completed
<i>SOCI 17 IN</i>	Babun Najah Orphanage Center	Ongoing
<i>SOCI 18 IN</i>	Darul Zahidin Orphanage Center	Ongoing
<i>SOCI 19 IN</i>	Kayee Kunyit Orphanage Center	Ongoing
<i>SOCI 20 IN</i>	Sukamakmur Orphanage Center	Ongoing
Merlin		
<i>HEAL 2 IN</i>	To prevent excess morbidity and mortality amongst the populations of tsunami affected regions of Aceh Province & Northern Sumatra	Ongoing
Ministry for Development of Disadvantaged Areas		
<i>INST 30 Multi</i>	Support for Poor and Disadvantaged Areas Project, Aceh and Nias	Design
Ministry of Health		
<i>HEAL – 0102 - UN</i>	Tsunami Emergency Relief Operations in NAD Province	Ongoing
Ministry of Marine Affairs and Fisheries (MAFF)		
<i>ECON 76 Bilat</i>	Rehabilitation of Fishing Activities	Ongoing
Ministry of the Environment		
<i>INFRA 98 Bilat</i>	Urgent improvement of the West coast Road Calang and Meulaboh	Design
<i>INFRA 124 IN</i>	British Columbia Demonstration Housing	Design
Mita Ileume Kota Sabang		
<i>ECON 60 UN</i>	Fishing Capacity Recovery – Sabang Island	Design
Mitra Lingkungan Duta Consult (MLD)		
<i>ECON 167 IG</i>	Supporting Recovery of Small Industries and Trades in Banda Aceh	Ongoing
Muslim Aid Indonesia		
<i>INFRA 3 LN</i>	Habitat (housing, water & sanitation) for fishing village communities	Ongoing
<i>SOCI 36 IN</i>	Muamalat	Ongoing
<i>INFRA 136 IN</i>	Rebuilding of Kindergarten	Ongoing
<i>INFRA - 0184 - IN</i>	Banda Aceh Flood Relief Flow Valves & Pump Stations	Study
NGOs		
<i>SOCI 21 UN</i>	UN World Food Programme	Design
<i>EDUC 79 IN</i>	English Education Program at Lamreh Elementary School, Kreung Raya Elementary School and Ruyung Elementary School, Sub-District: Mesjid Raya, District: Aceh Besar. Banda Aceh	Design
<i>EDUC 74 IN</i>	USINDO Aceh School Project	Design
<i>SOCI 35 IN</i>	Volleyball Field at Madrasah Aliyah Negeri Model Banda Aceh	Completed
Northwest Medical Teams International (NWMIT)		
<i>HEAL - 0107 - IN</i>	Community Dental hygiene training for children in Kuta Raja, Mesjid Raya and Leupung subdistricts.	Ongoing
<i>HEAL - 0109 - IN</i>	"Direct Medical and Dental Services in the subdistricts of Mesjid Raya, Kuta Raja, Leupung, Kampung Mulia (Banda Aceh) , Lamneuh (Kec Kotabaru) and Sabang.	Ongoing
<i>HEAL - 0110 - IN</i>	Institutional medical and health training in medical institutions (universities and colleges) in Banda Aceh. (Rumah Sakit Umum Zainoel Abidin) and Syiah Kuala University	Ongoing
<i>HEAL - 0111 - IN</i>	Nurse Training at Politeknik Kesehatan Banda Aceh	Ongoing
<i>HEAL - 0112 - IN</i>	PPNI Training Program for Nurses Working in Satellite Health Posts and Community Health Centers in Meulaboh	Ongoing
<i>HEAL - 0113 - IN</i>	Training of ER nurses in NAD Province in collaboration with the Ministry of Health	Ongoing
<i>SOCI – 0044 - IN</i>	Parenting Program	Ongoing
<i>SOCI – 0045 - IN</i>	Radio Opera Broadcast with Live roadshow and Comic follow up for Psi-Sos issues of Persons displaced by Tsunami of 2004.	Ongoing

*CAUTION: First Data Collection Round.
Validation in progress.*

RAN Database Summary Report

Partner / Project ID	Title	Project Status
ORPAD/Beujroeh		
<i>EDUC 61 IN</i>	See project EDUC 76 IN	Design
<i>EDUC 76 IN</i>	School Uniform Project in Peureumeue/Kecamatan Kaway XVI/Kabupaten Aceh Barat (PUTROU ACEH MULIA)	Design
<i>ECON 126 IN</i>	WOMEN INCOME GENERATING PROJECT FOR SMALL-SCALE TRADERS	Ongoing
OXFAM		
<i>INFRA 163 IN</i>	Project to support the reovery of tsunami amd earthquake affected communities though the reconstruction of Public health infrastructure and houses in Aceh and Nias.	Design
<i>ECON 143 IN</i>	Project to support the economic recovery of tsunami amd earthquake affected communities in Aceh and Nias	Design
PATH		
<i>HEAL 23 IN</i>	ACEH RECOVERY AND RECONSTRUCTION PROGRAM	Design
PT. McElhanney Indonesia		
<i>ECON 135 IN</i>	Aceh Jaya Agriculture Recovery Program	Design
<i>ECON 136 IN</i>	FHI's Livelihood Recovery for Desa Ujong Baroh, Kecamatan Johan Pahlawan, Kabupaten Aceh Barat	Design
<i>INFRA 170 IN</i>	Island	Design
<i>Cross - 0014 - IN</i>	Cross - 0014 - IN (Livelihood/Small Business Recovery,Agricultural Recovery,Education ,Infrastructure	Ongoing
Pak Dailami Nyak		
<i>ECON 90 IN</i>	Grant Agreement with Dailami Nyak for Reconstruction/re-equipping of the Labui Boat Building Works	Design
Palang Merah Indonesia (PMI)		
<i>HEAL 43 IN</i>	The Rehabilitation of the Blood Transfusion Unit and the Emergency Support to The Nangroe Aceh Darussalam Province	Design
<i>EDUC 104 LN</i>	Pengiriman bantuan Sepatu Orah Raga sebanyak 14.000 pasang	Design
<i>HEAL 124 IN</i>	Ambulance Services Rehabilitation in Nangroe Aceh Darussalam Province (PH6)	Ongoing
<i>HEAL 125 IN</i>	Temporary Living Centres for Displaced people in Aceh Besar (EMW4)	Ongoing
Pedulai Ekonomi Kerayatan Aceh		
<i>ECON 63 UN</i>	Fishing Capacity Recovery – Swak Indrapuri Meulaboh Aceh Barat	Design
Peoples' Crisis Centre (PCC)		
<i>ECON 78 IN</i>	Community Worker Capacity Building, Small Business and Micro Credit Project	Ongoing
Persatuan Perawat Nasional Indonesia (PPNI)		
<i>HEAL 58 IN</i>	Basic Health Services Program	Ongoing
Plan International		
<i>EDUC 46 IN</i>	School Reconstruction – Sekolah Dasar (SD) Kreung Raba, Kec. Lhok Nga, Aceh Besar	Approval
<i>EDUC 94 IN</i>	School Reconstruction – Sekolah Dasar (SD) Lam Gue-ue, Kec. Peukan Bada, Aceh Besar	Design
<i>INFRA 172 IN</i>	Lam Reh”	Design
<i>HEAL 98 IN</i>	Revitalization of Polindes in Peukan Bada sub-district, Acer Besar	Design
<i>HEAL 99 IN</i>	Revitalization of Posyandu in Aceh Besar District	Design
<i>INST 28 IN</i>	Birth Regstration Program in Masjid Raya, Aceh Besar district	Approval
<i>EDUC 93 IN</i>	EDUC 93 IN (batch) School Reconstruction – Sekolah Dasar (SD) Kreung Raba, Kec. Lhok Nga, Aceh Besar	Ongoing
<i>EDUC 96 IN</i>	EDUC 96 IN (batch 7) School Reconstruction – Sekolah Dasar (SD) Lambaro Neujid, Kec. Peukan Bada, Aceh Besar	Ongoing
Planete Urgence		
<i>SOCI 16 IN</i>	1. Computer classes for IDP women. 2. English classes for IDP women.3. Children activities (Play time)4. Information support for the Humanitarian Community in Aceh	Ongoing
Pompieri Sans Frontières		
<i>INST 5 IN</i>	Rehabilitation of the Civil Security / Fire Department of Banda Aceh	Ongoing
Private Enterprise Participation (PEP)		
<i>ECON 54 Bilat</i>	Private Enterprise Participation (PEP) Implementation I Project	Design
Professionals International (PI)		
<i>INFRA 82 IN</i>	Kecamatan Batee	Design
Project Concern International (PCI)		
<i>INFRA 46 IN</i>	Reconstruted local briges	Completed
<i>ECON 127 IN</i>	Livelihood Revitalisation (Cash-For-Work) for Disaster-Affected Families in Aceh (Donors: USAID/OFDA, UNDP, DAI, Private Sources)	Design
<i>HEAL 97 IN</i>	1 Mobile Clinics for Emergency Health Service Provision for the Aceh Quake and Tsunami Disaster	Design
<i>CROSS 7 IN</i>	Community-Led Actions for Recovery in Aceh (CLARA): Rebuilding Aceh's Shattered Social Fabric	Ongoing
Project HOPE		
<i>HEAL 59 IN</i>	Improving health & Health Services in Nagan Raya District after the Tsunami	Ongoing
<i>HEAL 61 IN</i>	Zainal Abidin Hospital Clinical Equipment and Training Support	Ongoing
<i>HEAL 62 IN</i>	Meuraxa Hospital Clinical Equipment and Training Support	Ongoing
<i>HEAL 63 IN</i>	Nagan Raya District Hospital Clinical Equipment and Training Support	Ongoing

CAUTION : First Data Collection Round.
Validation in progress.

RAN Database Summary Report

Partner / Project ID	Title	Project Status
RSUZA		
HEAL 82 Bilat	Jantho Hospital Project, Kota Jantho, Aceh Besar	Design
Rakata Action for Calang		
ECON 171 LN	Basic Potential Community Development Through Sustainable Livelihoods and Education Programme in Calang, Aceh Jaya	Ongoing
ReAct (Rebuilding Aceh Community Together)		
INFRA 143 LN	Rebuilding Aceh Community Together(Re:Act)	Design
SAB-SAS		
INFRA 99 Bilat	Sektor Air Belanda dukung Sektor Air Sumatera Wilayah Utara (SAB-SAS)	Ongoing
SOLIDARITES		
INFRA 4 IN	Assistance for the IDPs in Aceh Singkil	Design
EDUC 4 IN	8 Schools reconstruction and rehabilitation	Design
Samaritan's Purse		
ECON 88 IN	Samaritan's Purse Fishing Rehabilitation and Capacity Building	Design
ECON 89 IN	Skills Training Centre	Design
HEAL 64 IN	Child Development Program for Aceh Jaya District	Ongoing
INFRA 59 IN	Aceh Jaya & Nagan Raya Reconstruction and Livelihood Recovery Program	Ongoing
INFRA 192 IN	INFRA 192 IN (Batch 10) Permanent Housing Program for Nias in the subdistricts of Hiliduho and Gunung Sitoli	Ongoing
Sampoerna Foundation		
EDUC 91 IN	Freeman Foundation Aceh Relief Program	Design
Save the Children		
ECON 37 IN	Economic Recovery Assistance & Micro enterprise Development	Ongoing
EDUC 44 IN	Revitalization of community and district Educational System	Ongoing
INFRA 58 IN	Shelter and Water and Sanitation	Design
SOCI 22 IN	Child Protection	Ongoing
Savings Banks Foundation for International Cooperation (SBFIC)		
ECON 125 IN	Savings Banks Reconstruction Fund for South Asia	Ongoing
Sekretaris Daerah		
INST 7 Bilat	Governance Reform Support Phase (GRS) II	Ongoing
Soluziana S.A		
INFRA 173 IN	Sumatra	Ongoing
Spanish Red Cross		
SOCI - 0049 - IN	Indonesia Orphan and Family Fund (InOFF)	Ongoing
Swiss Agency for Development and Cooperation (SDC)		
INFRA 201 Bilat	INFRA 201 Bilat (Banda Aceh, Kecamatan Kuta Alma, Lampieneung 1 Borehole, water tower (GPS-Koordinates: N 05.33836° E 095.20635°)	Ongoing
INFRA 202 Bilat	INFRA 202 Bilat (Batch 10)	Ongoing
INFRA 203 Bilat	INFRA 203 Bilat (Batch 10 Aceh Barat, Kecamatan Johan Pahlawan, village Meulaboh)	Ongoing
Swiss Red Cross		
EDUC 115 IN	Orphan School Bantuan Bencana Alam, Banda Aceh	Ongoing
HEAL 123 IN	Sigli Heath Package	Ongoing
THW		
INFRA 40 Bilat	Rehabilitation of wells	Design
INFRA 41 Bilat	Upgrading of the spring in Glee Taron	Completed
INFRA 42 Bilat	Reconstruction Waterworks	Completed
INFRA 43 Bilat	Upgrading Spring Jantho	Ongoing
INFRA 44 Bilat	Rehabilitation of wells	Completed
EDUC 34 Bilat	Rehabilitation of the Library Badan Perpustakaan	Completed
EDUC 35 Bilat	Rehabilitation/Reconstruction TK Bhayangkari	Completed
EDUC 36 Bilat	Rehabilitation/Reconstruction SMP3Aceh Besar	Design
EDUC 37 Bilat	Rehabilitation/Reconstruction SDN97 Lamtemen Timur	Completed
HEAL 24 Bilat	Rehabilitation of the General Hospital	Completed
INFRA 39 Bilat	Rehabilitation of the City Council	Design
INFRA 117 IN	Building of 155 houses in Meunasah Bak Ue sub district Leupung	Design
INFRA 145 Bilat	Rehabilitation of springs and water intakes to re-establish sustainable water supply for the tsunami and earthquake victims of Simeulue island, Nanggroe Aceh Darussalam, Indonesia	Design
TNO Built Environment and Geosciences		
INFRA 153 IN	COASTPLAN Aceh-Nias – Geohazard preparedness by risk maps for sustainable redevelopment in the coastal zones Aceh and Nias	Ongoing

RAN Database Summary Report

Partner / Project ID	Title	Project Status
Terre des Hommes Italy		
<i>ECON 70 IN</i>	Emergency Rehabilitation of the Livelihood in the most affected Small-scale Fishery Communities in Bireuen District Nanggroe Aceh Darussalam	Completed
<i>EDUC 53 IN</i>	Supporting the recovery of the education system and improving the condition of school children affected by the tsunami disaster in Bireuen District	Completed
<i>EDUC 54 IN</i>	Supporting the resumption of pre-school and school activities / Reconstruction of 10 classrooms/teacher rooms with furniture and tools	Design
<i>HEAL 54 Bilat</i>	Terre des Hommes Italia	Design
<i>HEAL 41 IN</i>	Supporting the rehabilitation of the health system / Reconstruction and refurbishment of 6 village delivery centers, the primary health care center / Community-based psychosocial activities	Ongoing
<i>INFRA 76 IN</i>	Supporting the return of displaced families to their villages of origin / Reconstruction of 50 houses	Design
<i>SOCI 40 Bilat</i>	Community Based Project in Support to the mental well-being and the recovery of communities affected by the Tsunami disaster in Bireuen District, Aceh	Approval
The Mentor Initiative		
<i>HEAL 3 IN</i>	Rebuild capacity of Communicable Disease Control (CDC) of the Provincial Health Office (PHO) and 21 District Health Offices (DHO's) throughout the Province of Aceh	Ongoing
Tomorrow's Hope		
<i>EDUC 90 IN</i>	Project Tomorrow's Hope (Nias)	Design
Traditional Arts Lecture Organization		
<i>SOCI 14 LN</i>	Pengajaran Kesenian Tradisional Aceh Sebagai Alternatif Penanganan Trauma Pada Anak-anak Pengungsi dan desa-desa serta sekolah korban gempa dan tsunami di Kota Banda Aceh, Kab. Aceh Besar dan Kab. Aceh Jaya - Lamno	Ongoing
Triangle Generation Humanitaire (TGH)		
<i>EDUC 1 Bilat</i>	Psycho-social support through access to vocational trainings	Ongoing
<i>SOCI 3 IN</i>	Psychological support and strengthen social and community links into the displaced population of Tsunami victims	Ongoing
<i>ECON 121 IN</i>	Reactivation of the fishery sector: infrastructures and boats construction, cold chain and commercialization supply facilities in Aceh Besar	Ongoing
UAA-APHEDA		
<i>ECON 172 IN</i>	Aceh Trade Union Education Project	Ongoing
UMCOR		
<i>INFRA 112 IN</i>	Integrated Rehabilitation of Tsunami Affected Communities (IRTAC) Project	Ongoing
UN-HABITAT		
<i>INFRA 165 UN</i>	Aceh-Nias Settlements Support Programme (ANSSP)	Ongoing
UNDP		
<i>ECON 55 Bilat</i>	Canadian Support to Aceh Emergency Response and Transitional Recovery (CSAERTR)	Ongoing
<i>SPAT 10 UN</i>	Assistance to the Aceh Reconstruction and Rehabilitation Authority (BRR) in relation to Relocation in Tsunami-Affected NAD	Ongoing
UNESCO		
<i>SOCI 38 UN</i>	Aceh	Ongoing
<i>ECON 110 UN</i>	Mitigation of post-tsunami environmental threats on Tropical Rainforest of Sumatra World Heritage site and adjacent conservation areas, Aceh Province, Indonesia	Ongoing
<i>SOCI 42 UN</i>	Rebuilding Library Capacity in Banda Aceh	Design
UNFPA		
<i>HEAL 79 UN</i>	Reproductive Health, Psychosocial Support, Provision of personal hygiene kits, Health Promotion, Prevention and Management of Gender Based Violence (GBV), and Census	Ongoing
UNHCR		
<i>CROSS 16 UN</i>	Pilot Project in Kecamatan Krueng Sabe	Ongoing
<i>INFRA - 0179 - UN</i>	Permanent shelter programme in Calang, District of Aceh Jaya.	Ongoing
UNICEF		
<i>EDUC 23 UN</i>	Basic Education	Design
<i>HEAL 19 UN</i>	Provinces	Design
<i>SOCI 13 UN</i>	Child Protection for Nanggroe Aceh Darussalam and North Sumatra Provinces	Ongoing
UNSYIAH		
<i>EDUC 56 IN</i>	Internet Base Learning Support System for Unsyiah	Design
<i>EDUC 85 IN</i>	Student Teachers as Temporary Teachers for Aceh Jaya (IN-18-01)	Ongoing
<i>HEAL 77 IN</i>	Health Management Course-Decentralizing Health Services	Design

RAN Database Summary Report

Partner / Project ID	Title	Project Status
USAID		
ECON 117 IN	Support for Peaceful Democratization (SPD), Community-Based Recovery (CBR) Initiative and Small Grants Program	Design
INFRA 120 IN	Municipal Finance	Design
ECON 96 IN	Watershed Management and Biodiversity Conservation	Ongoing
INFRA 119 IN	Environmental Services Delivery-Drinking Water Supply and Sanitation	Design
ECON 103 IN	USAID & Chevron Alliance for Vocational and Technical Education	Design
EDUC 72 Bilat	USAID Aceh Teacher Training Support	Design
INFRA 118 IN	Banda Aceh-Meulaboh Road and Bridge Project	Design
EDUC 73 IN	USAID Decentralized Basic Education (DBE)	Ongoing
United Diversity Forum		
INFRA 190 IN	INFRA 190 (Batch 10) Sirombu Village House and Boat Project	Ongoing
WALHI		
ECON 77 IN	Environmental resource centre development and capacity building project	Procurement
Walikota Banda Aceh		
ECON 18 IN	Banda Aceh Fishing Market Vitalization	Ongoing
Winrock International		
ECON 36 IN	Aceh Fisheries Rehabilitation and Development Project	Design
World Food Programme (WFP)		
INFRA 200 UN	INFRA 200 UN (BATCH 10) - WFP Logistic	Ongoing
World Health Organization (WHO)		
HEAL 102 UN	Tsunami Emergency Relief Operations in NAD Province	Design
World Relief		
ECON 69 UN	Kerung Raya livelihoods, fishing and small grant project	Ongoing
EDUC 59 IN	Formal Schools Rehabilitation Project	Design
HEAL 44 IN	Meulaboh School of Nursing (Akademy Perawatan, Meulaboh – AkPer)	Ongoing
INFRA 144 IN	Mesjid Raya Housing Reconstruction and Rehabilitation Project	Ongoing
World Vision		
EDUC 10 IN	Lamno: Education Hardware-Rehabilitation	Design
EDUC 11 IN	Lamno: Education Software	Ongoing
EDUC 12 IN	Lhoong: Education Hardware	Ongoing
EDUC 13 IN	Lhoong: Education Software	Ongoing
EDUC 14 IN	Meulaboh Education Project	Ongoing
EDUC 15 IN	Nias: Education Project	Ongoing
EDUC 7 IN	Banda Aceh/Aceh Besar: Education	Completed
EDUC 8 IN	Education Software	Design
EDUC 9 IN	Lamno: Education	Ongoing
HEAL 10 IN	Health, Banda Aceh	Ongoing
HEAL 11 IN	Lamno: Health Project	Ongoing
HEAL 12 IN	Lamno: Health Software	Ongoing
HEAL 13 IN	Lhoong: Health Hardware	Completed
HEAL 14 IN	Lhoong: Health Software	Ongoing
HEAL 15 IN	Meulaboh: Health Project	Ongoing
SOCI 6 IN	Banda Aceh/Aceh Besar: Child Friendly Activities	Ongoing
SOCI 7 IN	Banda Aceh/Aceh Besar: Food Distribution	Design
SOCI 8 IN	Lamno - Child Protection	Ongoing
HEAL 9 IN	Banda Aceh/Aceh Besar: Health Hardware	Ongoing
INFRA 13 IN	Banda Aceh - Shelter	Ongoing
INFRA 14 IN	Banda Aceh/Aceh Besar: TLC and Community Buildings Shelter	Ongoing
INFRA 15 IN	Banda Aceh/Aceh Besar: Water/Sanitation	Ongoing
INFRA 16 IN	Lamno: Permanent Housing	Ongoing
INFRA 17 IN	Lamno: TLCs	Completed
INFRA 18 IN	Lamno: Water and Sanitation	Ongoing
INFRA 19 IN	Lhoong: Permanent Housing	Ongoing
INFRA 20 IN	Lhoong: TLC Shelter	Completed
INFRA 21 IN	Lhoong: Water and Sanitation Activities	Ongoing
INFRA 23 IN	Meulaboh: Temporary and Permanent Housing	Ongoing
INFRA 24 IN	Meulaboh: Water and Sanitation Project	Ongoing
SOCI 10 IN	Meulaboh: Child Friendly Activities	Ongoing
SOCI 9 IN	Lhoong: Child Friendly Activities	Ongoing
EDUC 100 IN	Nias: Education Software Support	Design
INFRA 137 IN	Nias Water, Sanitation and Education Rehabilitation Project	Ongoing
ECON 13 IN	Banda Aceh/Aceh Besar: Economic Development	Ongoing
ECON 14 IN	Lamno: Economic Recovery/Livelihoods	Ongoing
ECON 15 IN	Lhoong: Economic Recovery/Livelihoods	Ongoing
ECON 17 IN	Meulaboh: Economic Recovery/Livelihoods	Ongoing

*CAUTION: First Data Collection Round.
Validation in progress.*

RAN Database Summary Report

Partner / Project ID	Title	Project Status
YADESA		
INFRA 106 Bilat	Provision of Communal Water and Sanitation Facilities for the Tsunami Victims in Lhoong	Design
YAKKUM Emergency Unit (YEU)		
INFRA 138 LN	Project ASRE 51: Emergency Response in Banda Aceh, Aceh Barat, Nagan Raya, and Aceh Utara: Clean Water and Sanitation Sector	Design
INFRA 174 LN	Project ASRE 51: Emergency Response in Aceh Besar, Aceh Barat, Nagan Raya, Aceh Utara and Nias: Clean Water and Sanitation Sector	Completed
ECON 145 LN	Project ASRE 51: Emergency Response in Aceh Besar, Nagan Raya, Aceh Utara, and Nias: Livelihood Recovery Sector	Ongoing
HEAL – 0103 - IN	(Batch 8) HEAL – 0103 - IN(Project ASRE 51: Emergency Response in Aceh Besar, Aceh Barat, Nagan Raya, Aceh Utara and Nias: Health Sector)	Ongoing
HEAL - 104 - LN	(BATCH 8) HEAL-104-LN Project ASRE 51: Emergency Response in Aceh Besar,Aceh Utara, Aceh Barat and Nias for Tsunami and Earthquake: Psychosocial Sector	Ongoing
YBI & Techni Service Company		
INFRA 121 IN	Recycle Aceh	Design
INFRA 167 LN	YBI Housing Reconstruction Project	Design
YIPD		
INST 15 IN	Yayasan Inovasi Pemerintahan Daerah – YIPD	Design
Yayasan Bina Perdamaian Internasional Indonesia		
INST 14 LN	Peace Brigades International Indonesia Project Yayasan Bina Perdamaian Internasional Indonesia	Ongoing
Yayasan Dian Desa		
ECON 13 IN	Banda Aceh/Aceh Besar: Economic Development	Ongoing
Yayasan Ikan Tenggiri		
ECON 59 UN	Fishing Capacity Recovery – Muara Batu, Aceh Utara	Design
Yayasan Karya Banda Sejahtera		
ECON 115 IN	Tsunami Micro Finance Initiative. It will introduce Micro Finance to the Tsunami affected peoples of Aceh province	Ongoing
Yayasan Kasih Peduli Masyarakat Indonesia (YKPMI)		
INFRA 150 IN	Reconstruction Desa Hiligawoni, Bitaya, Ononamolo Kecamatan Lahewa, Nias	Design
Yayasan Lembaga Ekonomi Panta Pesisir		
ECON 67 UN	Assistance for Small Scale Fish Processing Farmers in Pidie	Design
Yayasan MAS		
ECON 158 IN	ECON 158 IN (BATCH 10) - Membangun kembali Desa Cot Riwayatdi Aceh Besar dan Proyek Livelihood	Ongoing
INFRA 196 IN	INFRA 196 IN (Batch 10) Yayasan MAS Infrastructure Sector	Ongoing
Yayasan Masyarakat Makmur Mitra Adil (MAMAMIA)		
INFRA 89 IN	Program Rekonstruksi Rumah Lhoong (PRR-L)	Ongoing
Yayasan Mitra Dhuafa		
ECON 115 IN	Tsunami Micro Finance Initiative. It will introduce Micro Finance to the Tsunami affected peoples of Aceh province	Ongoing
Yayasan Pelangi		
ECON 62 UN	Fishing Capacity Recovery – Simeulue Island	Design
Yayasan Pelayanan Fajar Harapan (YFPF)		
SOCI 57 LN	SOCI 57 LN (Batch 10) Pemulihan trauma anak Aceh dan Nias korban gempa/tsunami.	Ongoing
Yayasan Pengembangan Kawasan		
ECON 61 UN	Fishing Capacity Recovery – Kecamatan Samatiga, MeulabohAceh Barat	Design
Yayasan Tanggul Bencana di Indonesia (YTBI)		
ECON 155 LN	ECON 155 LN (BATCH 10) - PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
ECON 154 IN	ECON 154 IN (BATCH 10) - PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
EDUC 110 LN	EDUC 110 LN (BATCH 10) - PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
HEAL 117 LN	HEAL 117 LN (BATCH 10) - PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
INFRA 191 LN	INFRA 191 LN (Batch 10) PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
INST 33 LN	INST 33 LN (BATCH 10) - PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
SOCI 58 LN	SOCI 58 LN (BATCH 10) - PROGRAM PENANGGULANGAN BENCANA GEMPA BUMI DAN TSUNAMI ACEH DAN NIAS	Ongoing
(YUA)		
INFRA 151 IN	Wells Cleaning, Drainage Rebuild, and Bridge Reconstruction in Samalanga	Ongoing

RAN Database Summary Report

Partner / Project ID	Title	Project Status
Yayasan sosial KREASI		
<i>EDUC 28 LN</i>	Dormitory for Female Students	Ongoing
<i>EDUC 29 LN</i>	Build a Kindergarten	Completed
<i>EDUC 30 LN</i>	Support Reading and Activity Center	Ongoing
<i>EDUC 31 LN</i>	School Uniforms, Supplies and Textbook Distribution	Completed
<i>EDUC 32 LN</i>	Junior High/LAB School --- CANCELLED	Suspended
<i>EDUC 33 LN</i>	Teacher Training Center Support	Completed
<i>HEAL 22 LN</i>	Mobile Health Clinics	Completed
<i>INFRA 36 LN</i>	Building to house 4 Labs	Ongoing
<i>INFRA 37 LN</i>	Shelter/Construction	Completed
<i>INFRA 38 LN</i>	Water Sanitation	Ongoing
<i>ECON 23 LN</i>	Agriculture	Ongoing
<i>ECON 24 LN</i>	Brick Factory Project	Ongoing
Yokohama Waterworks Bureau		
<i>INFRA 126 Bilat</i>	Provision of Submersible Water Supply Pumps	Design
partner to be define		
<i>INFRA 90 IN</i>	<i>Reconstruction of 95 houses, Angkeo, Simeulue</i>	<i>Ongoing</i>
<i>INST 8 Bilat</i>	<i>Canadian Support to Kecamatan Development Project in Aceh and North Sumatra (KASKEDEPAN)</i>	<i>Design</i>

RAN Database Summary Report

14. Organisations represented in RAN Database

There are 509 organisations listed either as a donor or as a partner in the database as of the 1st of December.

#	Organisation Name	Type	Access to RAN Database
1	Abbe Pierre Foundation	INGO	No
2	Abdul Lateef Jamil Group	Private Sector	No
3	ACE (Association for Community Empowerment)	INGO	No
4	ACE INA Foundation	INGO	No
5	Aceh Institute	National NGO	No
6	Aceh Relief	National NGO	Yes
7	ACF	INGO	Yes
8	ACT International	INGO	Yes
9	ACTED	INGO	Yes
10	ADH	INGO	No
11	Adopt A Doctor (AAD)	INGO	No
12	ADRA (ADVENTIST DEVELOPMENT AND RELIEF AGENCY) - Germany	INGO	No
13	AFP	INGO	No
14	Agence de l'Eau Adour-Garonne, France	INGO	No
15	Agricultural Services	Other	No
16	AIFO	INGO	Yes
17	AIG	INGO	No
18	AIPRD	Bilateral	Yes
19	AIRO	INGO	No
20	AJWS	INGO	No
21	Akron Deutschland Hilft	INGO	No
22	Akzo Nobel Chemicals Singapore	Private Sector	No
23	Alanis Morrisett	Other	No
24	Alisei	INGO	No
25	Allianz employees	INGO	No
26	AMDA	INGO	Yes
27	American JJDC	INGO	No
28	American JWS	INGO	No
29	American Overseas Medical Aid Association (AOMAA)	INGO	No
30	American Red Cross	IO	Yes
31	AmeriCares	IFI	No
32	AMI FRANCE	INGO	Yes
33	AMSA	INGO	No
34	AMURT	INGO	No
35	Anwarsyah	INGO	No
36	Architectes de l'urgence	INGO	No
37	Arcilla Research	INGO	No
38	Asian Development Bank	IFI	Yes
39	Associative Funds	INGO	No
40	Astra Honda Motor	Private Sector	No
41	ATLAS Logistique	INGO	Yes
42	AusAid	Bilateral	No
43	Austcare	INGO	No
44	AUSTCARE	INGO	Yes
45	Austin (US NGO)	INGO	No
46	Australia	Bilateral	No
47	Australian Red Cross	IO	Yes
48	Austria	Bilateral	No
49	AVON	INGO	No
50	AYUNTAMIENTO DE MADRID	Bilateral	No
51	AYUNTAMIENTO DE MANRESA	Bilateral	No
52	AYUNTAMIENTO DE SANTA CRUZ DE TENERIFE	INGO	No
53	Ayuntamiento de Valdemoro	INGO	No
54	Badan Penanggulangan Bencana (BPB)	Government Agency	No
55	Badan Pertanahan Nasional	Government Agency	No
56	Bainbridge Island Tsunami Relief Funds (BISTRF)	INGO	No
57	Bank Danamon	Private Sector	No
58	Bapal	Other	No
59	BAPPENAS	Government Agency	No
60	Baxter	Bilateral	No
61	Belgian Red Cross	IO	Yes
62	Belgian Red Cross Fr	IO	Yes
63	Belgium	Bilateral	No
64	BGR/GTZ	INGO	No

RAN Database Summary Report

#	Organisation Name	Type	Access to RAN Database
65	BICG	INGO	No
66	BMZ	INGO	No
67	British American Tobacco - Indonesia	Private Sector	No
68	British Red Cross	IO	Yes
69	Brother's Brother Foundation	INGO	No
70	BRR	Government Agency	Yes
71	Build Change	INGO	Yes
72	Bupati Aceh Besar	Government Agency	No
73	CAM	INGO	Yes
74	Canada	Bilateral	Yes
75	Canadian Embassy	INGO	No
76	Canadian Red Cross	IO	Yes
77	CARDI NRC	INGO	Yes
78	CARE	INGO	Yes
79	Caritas Austria	INGO	Yes
80	Caritas Bozen, Italy	INGO	No
81	Caritas Czech Republic	INGO	Yes
82	CARITAS GERMANY	INGO	Yes
83	Caritas Portugal	INGO	No
84	Caritas Sibolga	National NGO	No
85	CARITAS SWITZERLAND	INGO	Yes
86	CCP	Academic Institutions	No
87	Center for Mind-Body Medicine (CMBM)	Academic Institutions	No
88	Center for Research and Community Development	Academic Institutions	No
89	CH Solidarity Chain	INGO	No
90	CHF International	INGO	Yes
91	ChildFund Australia	INGO	No
92	ChildFund New Zealand	INGO	No
93	Children of Sumatra	INGO	No
94	Children on the Edge	INGO	Yes
95	China	Bilateral	No
96	Chinese Red Cross	IO	Yes
97	Christian Aid Ministries	INGO	No
98	Christian Children's Fund	INGO	Yes
99	Christian Surfers	INGO	No
100	CIDA	Bilateral	Yes
101	Cis Council	Other	No
102	City of Phoenix	Other	No
103	CITYNET	Other	No
104	Clinical Engineering	INGO	No
105	Coastal Resources Center(University of Rhode Island)	Academic Institutions	No
106	Compassion International	INGO	No
107	Concern for Kids	INGO	No
108	Concern Worldwide	INGO	Yes
109	Conservation International	INGO	No
110	CORDAID the Netherland	INGO	No
111	Counterpart International	INGO	No
112	CRCWC	Other	No
113	Credit Suisse First Boston	Private Sector	No
114	CRS	INGO	Yes
115	CRWRC	INGO	No
116	CWS	INGO	Yes
117	DAI (Development Alternatives Incorporated)	Private Sector	No
118	DANIDA	Bilateral	No
119	Danish Red Cross	IO	Yes
120	DEA	INGO	No
121	DEC (UK Disaster Emergency Committee)	Bilateral	No
122	Dell Foundation	Private Sector	No
123	Denmark	Bilateral	No
124	Departement of Public Works	Government Agency	No
125	Development Cooperation Ireland	Bilateral	No
126	Diageo	Private Sector	No
127	Diakonie Emergency Aid (DEA)	INGO	No
128	Dinas Kehutanan	Government Agency	No
129	Dinas Pekerjaan Umum	Government Agency	Yes
130	Dinas Pemuda dan Olahraga	Government Agency	Yes
131	Dinas Perhubungan	Government Agency	Yes
132	Dinas Perikanan Peternakan Perikanan dan Kelautan Kota Banda Aceh	Government Agency	No
133	Dinas Perindustrian dan Perdagangan Aceh Besar	Government Agency	No
134	Dinas Perindustrian dan Perdagangan Banda Aceh	Government Agency	No
135	Dinas Sosial	Government Agency	No

*CAUTION: First Data Collection Round.
Validation in progress.*

RAN Database Summary Report

#	Organisation Name	Type	Access to RAN Database
136	Dinas Sumber Daya Air	Government Agency	No
137	DINASKERTRANS	Government Agency	No
138	Diocese	Other	No
139	Diponegoro University – Semarang	Academic Institutions	No
140	DIPT	Other	No
141	DIPUTACION DE BARCELONA	Other	No
142	Direct Relief International	IO	No
143	DLA Piper-Rudnick	Other	No
144	EC (European Commission)	Bilateral	No
145	ECHO (European Commission Humanitarian Aid Office)	Bilateral	Yes
146	Education International	INGO	Yes
147	Educational Development Center (EDC)	INGO	No
148	Enfants Refugees du Monde (ERM)	INGO	Yes
149	EOM/SHO	INGO	No
150	EPOS	INGO	No
151	Express Way	INGO	No
152	Exxon-Mobile	Private Sector	No
153	FAO (United Nations Food and Agriculture Organization)	UN	Yes
154	Farnow	Private Sector	Yes
155	Fauna and Flora International (FFI)	INGO	Yes
156	Feel the Love	Other	No
157	FFI	INGO	No
158	FIAS	INGO	No
159	FIG-Indonesia	Other	No
160	Finland	Bilateral	No
161	Fishery Department Bireuen	Government Agency	No
162	FKIP Unsyiah	INGO	No
163	Flora Family Foundation	INGO	No
164	Fondation de France	INGO	No
165	Fondation MACIF(FR)	INGO	No
166	Fondation Suez (FR)	INGO	No
167	Food for the Hungry International (FHI)	INGO	Yes
168	ForesTrade	INGO	No
169	Forum Bangun Aceh(FBA)	National NGO	Yes
170	Forum LSM Aceh	INGO	No
171	France (Other)	Bilateral	No
172	Freeman Foundation	INGO	No
173	French Collective for children	INGO	No
174	French Embassy	Bilateral	No
175	French National Olympic Committee	INGO	No
176	French Red Cross	IO	Yes
177	GAA and Hivos funds	IFI	No
178	Gary Samatimbang	Other	No
179	Gates Foundation	Private Sector	No
180	GenAssist	INGO	No
181	GENERALITAT DE CATALUNYA	Other	No
182	Gerber	Other	No
183	German Agro Action (GAA)	INGO	No
184	German Embassy	Bilateral	No
185	German Institution	Other	No
186	German Red Cross	IO	Yes
187	German Savings Banks Finance Group	Other	No
188	Germany (Other)	Bilateral	No
189	GKI	National NGO	No
190	Global Greengrants Fund	Other	No
191	Global Thematic Humanitarian Response	Other	No
192	GOBIERNO DE NAVARRA	Other	No
193	Goldman Sachs Japan	Private Sector	No
194	Gong Pasee	National NGO	No
195	Grameen Foundation	INGO	Yes
196	Grameen Foundation USA	INGO	Yes
197	Gruppo Volontariato Civile (GVC)	INGO	Yes
198	GTZ	INGO	Yes
199	Habitat for Humanity Indonesia	INGO	Yes
200	Handicap International	INGO	Yes
201	HANUMA	National NGO	No
202	Health Department	Government Agency	No
203	Heks - Swiss	INGO	No
204	Helen Keller International	INGO	Yes
205	Help e.V. Germany	INGO	No
206	Helping Hands Foundation	INGO	Yes

CAUTION : First Data Collection Round.
Validation in progress.

RAN Database Summary Report

#	Organisation Name	Type	Access to RAN Database
207	Hess	INGO	No
208	Hilfswerk Austria	INGO	No
209	HJ Heinz Company Foundation	Private Sector	No
210	Hong Kong Red Cross	IO	Yes
211	HOPE International	INGO	No
212	IACO	INGO	No
213	IAIN AR-RANIRY – The State Institute for Islamic Studies – Banda Aceh	Academic Institutions	No
214	IBU4ACEH	National NGO	Yes
215	ICCO	INGO	No
216	ICMC	INGO	Yes
217	IDEP	National NGO	Yes
218	IDES	INGO	No
219	IFAD (International Fund for Agricultural Development)	INGO	No
220	IFC (International Finance Corporation)	IO	Yes
221	IFRC (International Federation of Red Cross and Red Crescent Societies)	IO	Yes
222	IMC (International Medical Corps)	INGO	Yes
223	Indonesia	Bilateral	No
224	Indonesian International Education Foundation (IIEF)	INGO	No
225	International AID	INGO	No
226	International Baccalaureate Organisation(IBO)	INGO	No
227	International Labour Organization (ILO)	UN	Yes
228	International Organization for Migration (IOM)	IO	Yes
229	International Relief and Development (IRD)	INGO	Yes
230	International SOS	INGO	Yes
231	Internationale Weiterbildung und Entwicklung, gGmbH	INGO	No
232	IOM (International Organization for Migration)	IO	Yes
233	IPS NGO	INGO	No
234	IRC (International Rescue Committee)	INGO	Yes
235	Ireland	Bilateral	No
236	Irish Red Cross	IO	Yes
237	IRM NAD (Ikatan Remaja Muhammadiyah Nanggroe Aceh Darussalam)	National NGO	No
238	Islamic Relief	INGO	Yes
239	Italian Cooperation	Bilateral	Yes
240	Italy (Other)	Bilateral	No
241	ITB	INGO	No
242	Jakarta International School	Other	No
243	Japan (Other)	Bilateral	No
244	Japanese Red Cross	IO	Yes
245	Jaringan Kasih (JARKAS)	National NGO	Yes
246	JARKAS	INGO	No
247	Jessica Fund*	INGO	No
248	JICA	Government Agency	Yes
249	JICS	INGO	No
250	JIS Cares - Peduli	INGO	No
251	Johanniter-Unfall-Hilfe (JUH)	INGO	No
252	Johnson and Johnson	Private Sector	No
253	JRS	INGO	Yes
254	Jumadi	INGO	No
255	Junta de Comunides. DE CASTILLA LA MANCHA	Other	No
256	Keio University	Academic Institutions	No
257	Ken Atlee	Other	No
258	KfW	Bilateral	Yes
259	Kindernothilfe (KNH) Germany	INGO	No
260	KOICA	INGO	No
261	Kolaborasi Nurani	INGO	No
262	Komisi Independen Pemilu (KIP)	Government Agency	Yes
263	Komite Rehabilitasi dan Rekonstruksi Jambo Mesjid	National NGO	No
264	Komunitas Indonesia Bersatu - Stuttgart	INGO	No
265	Korea, Republic of	Bilateral	No
266	Korean Red Cross	IO	Yes
267	KOTIB NAD-SUMUT/ Dina Kartika Sari	National NGO	No
268	Latter-day Saint Charities (LDSC)	INGO	No
269	Lavelle Fund for the Blind	INGO	No
270	Lazarus HW	INGO	No
271	LBH Anak	National NGO	No
272	Lembaga Kerjasama Indonesia Jerman (LKIJ)	Bilateral	Yes
273	Leuser International Foundation	INGO	Yes
274	Libra Foundation	INGO	No
275	Local Empowerment Assistance Project Inc (LEAP)	Private Sector	No
276	Local Governance Support Program (LGSP)	INGO	Yes
277	Malaysia	Bilateral	No

CAUTION: First Data Collection Round.
Validation in progress.

RAN Database Summary Report

#	Organisation Name	Type	Access to RAN Database
278	Malteser International	INGO	Yes
279	MALV (Moslem Association of Leigh Valley), USA	INGO	No
280	Matahari	Government Agency	No
281	MDTF	IO	Yes
282	MDTFANS	Other	No
283	Medecins Du Monde	INGO	Yes
284	Medecins Sans Frontieres-Belgium	INGO	Yes
285	Medecins Sans Frontieres-France	INGO	Yes
286	Medical Library	Other	No
287	Medicos del Mundo	INGO	Yes
288	Mees Pierson Asia	Other	No
289	Mennonite Central Committee (MCC)	INGO	Yes
290	Merck	INGO	No
291	Mercy Corps International	INGO	Yes
292	Mercy Malaysia	INGO	Yes
293	MERCY USA	INGO	Yes
294	Merlin	INGO	Yes
295	Meyrieu Laboratories	Academic Institutions	No
296	Michelin	Private Sector	No
297	Ministry for Development of Disadvantaged Areas	Government Agency	No
298	Ministry of Health	Government Agency	No
299	Ministry of Marine Affairs and Fisheries (MAFF)	Government Agency	No
300	Ministry of the Environment	Government Agency	No
301	Misereor	INGO	No
302	Mita Ileume Kota Sabang	National NGO	No
303	Mitra Lingkungan Duta Consult (MLD)	National NGO	No
304	MMAF	INGO	No
305	MSF Holland	INGO	Yes
306	MSF-Belgium	INGO	No
307	Muslim Aid	INGO	Yes
308	Nachbar in Not	Other	No
309	Neighbour in Need	INGO	No
310	Netherlands	Bilateral	No
311	Netherlands Red Cross	IO	Yes
312	New Zealand	Bilateral	No
313	Nike	Private Sector	No
314	Norlink	INGO	No
315	Northwest Medical Teams International (NWMT)	INGO	Yes
316	Norway (Other)	Bilateral	No
317	Norwegian Lutheran Ministry	INGO	No
318	Norwegian MFA	Bilateral	No
319	Norwegian Ministry of Foreign Affairs	Bilateral	No
320	Norwegian Red Cross	IO	Yes
321	Norwegian Refugee Council	INGO	No
322	NOVIB	INGO	No
323	NRC	INGO	No
324	NYC Public Schools	Other	No
325	NZAID	Government Agency	No
326	Oak Foundation	INGO	No
327	OB/GYN	INGO	No
328	Obor Foundation	INGO	No
329	OCHA (Office for Coordination of Humanitarian Affairs)	UN	No
330	OFDA	Bilateral	No
331	OIKOS Cooperacao e Desenvolvimento	INGO	Yes
332	OndulineGroup	INGO	No
333	Opportunity International	INGO	No
334	ORPAD/Beujroeh	INGO	No
335	OTI	Other	No
336	OXFAM	INGO	Yes
337	Packard Foundation	Other	No
338	Pak Dailami Nyak	Other	No
339	Palang Merah Indonesia (PMI)	IO	Yes
340	Pander Sitindaon	Other	No
341	Partridge Foundation	Other	No
342	PATH	INGO	No
343	PBI	Other	No
344	Peace Winds Japan	INGO	Yes
345	Pedulai Ekonomi Kerayatan Aceh	Other	No
346	Penang Office of Human Development	Government Agency	No
347	Peoples' Crisis Centre (PCC)	INGO	No
348	PepsiCo Foundation	Private Sector	No

CAUTION: First Data Collection Round.
Validation in progress.

RAN Database Summary Report

#	Organisation Name	Type	Access to RAN Database
349	Persatuan Perawat Nasional Indonesia (PPNI)	Other	No
350	Perusahaan Daerah Pembangunan Aceh	Government Agency	No
351	PESADA	Academic Institutions	No
352	Petronas	Private Sector	No
353	Petronita	Private Sector	No
354	Pfizer	Private Sector	No
355	PKPA	INGO	Yes
356	Plan International	INGO	Yes
357	Planete Urgence	INGO	Yes
358	Pompiers Sans Frontières	INGO	Yes
359	Portugal	Bilateral	No
360	Price Waterhouse Cooper	Private Sector	No
361	PRINCIPADO DE ASTURIAS	Other	No
362	Private Enterprise Participation (PEP)	Private Sector	No
363	Professionals International (PI)	INGO	Yes
364	Project Concern International (PCI)	INGO	Yes
365	Project HOPE	INGO	Yes
366	Project HOPE	INGO	Yes
367	PSFCI (Pharmaciens Sans Frontières Comité International)	INGO	No
368	PT Penajati	Private Sector	No
369	PT SUCOFINDO	Private Sector	No
370	PT. Astra Honda Motor	Private Sector	No
371	PT. McElhanney Indonesia	Private Sector	No
372	PT. Mitra Lingkungan Dutaconsult (MLD)	Private Sector	No
373	PUGAR	INGO	No
374	Putu Madhuvidya	INGO	No
375	Qatar Charitable Society	INGO	No
376	R & D STEVE Goode	Other	No
377	Rakata Action for Calang	National NGO	Yes
378	Razali Hasan	Other	No
379	ReAct (Rebuilding Aceh Community Together)	INGO	No
380	Relief International	INGO	No
381	Rotary-Club SYKE E.V Germany	INGO	No
382	RSUZA	INGO	No
383	RTI (Research Triangle Institute, International)	INGO	No
384	SAB-SAS	INGO	No
385	Sacred Bridge Foundaion	INGO	No
386	Saddleback	INGO	No
387	Samaritan's Purse	INGO	Yes
388	Sampoerna Foundation	Private Sector	Yes
389	Sanofi	INGO	No
390	Save the Children	INGO	Yes
391	Save the Children Italy	INGO	Yes
392	Save the Children Netherlands	INGO	Yes
393	Save the Children New Zealand	INGO	Yes
394	Save the Children Norway	INGO	Yes
395	Save the Children Spain	INGO	Yes
396	Save the Children Sweden	INGO	Yes
397	Savings Banks Foundation for International Cooperation (SBFIC)	Private Sector	No
398	Secours Catholique	Other	No
399	Sekretaris Daerah	Other	No
400	SGP-GEF Indonesia	National NGO	No
401	SIDA	Bilateral	No
402	Sight and Life Task Force	INGO	No
403	Sigrid rausing Trust	INGO	No
404	Singapore	Bilateral	No
405	Slovak Red Cross	IO	Yes
406	Small Kindness	INGO	No
407	SOLIDARITES	INGO	No
408	Soluziana S.A	INGO	No
409	Spain	Bilateral	No
410	Spanish Red Cross	IO	Yes
411	Staf Pengajar Cardiff University, UK	Academic Institutions	No
412	Starr Foundation	INGO	No
413	Sunspirit	INGO	No
414	SurfAid	INGO	No
415	SurfAid International	INGO	No
416	Susila Dharma International	INGO	No
417	SV	INGO	No
418	Sweden	Bilateral	No
419	Swiss Agency for Development and Cooperation (SDC)	Government Agency	No

CAUTION : First Data Collection Round.
Validation in progress.

RAN Database Summary Report

#	Organisation Name	Type	Access to RAN Database
420	Swiss Embassy	Bilateral	No
421	Swiss Government	Bilateral	No
422	Swiss Red Cross	IO	Yes
423	Swisscontact	INGO	No
424	Switzerland	Bilateral	No
425	Taiwan	Bilateral	No
426	TBA	INGO	No
427	Telluride Foundation	INGO	No
428	Terre Des Hommes	INGO	No
429	Terre des Hommes Italy	INGO	Yes
430	The Body Shop International	Private Sector	No
431	The Church of Jesus Christ of Latter-day Saints	INGO	Yes
432	The Ford Foundation	INGO	No
433	The JOHANNITER	INGO	No
434	The Mentor Initiative	INGO	Yes
435	The Michael and Susan Dell Foundation	INGO	No
436	The Queensland Government	Bilateral	No
437	The Samdhana Institute	INGO	No
438	THW	INGO	No
439	TNO Built Environment and Geosciences	INGO	No
440	Tomorrow's Hope	INGO	Yes
441	Traditional Arts Lecture Organization	National NGO	No
442	Triangle (France's NGO)	INGO	No
443	Triangle Generation Humanitaire (TGH)	INGO	Yes
444	Tsunami Partnership Initiative of the Germany	INGO	No
445	UAA-APHEDA	INGO	Yes
446	UAA-APHEDA	INGO	Yes
447	UID	INGO	No
448	UMCOR	INGO	Yes
449	UNDP (United Nations Development Programme)	UN	Yes
450	UNESCO (United Nations Educational, Scientific and Cultural Organization)	UN	Yes
451	UNFPA	UN	No
452	UN-HABITAT	UN	Yes
453	UNHCR (United Nations High Commissioner for Refugees)	UN	Yes
454	UNICEF (United Nations Children's Fund)	UN	Yes
455	UNIDO	UN	No
456	UNIFEM	UN	Yes
457	United Diversity Forum	INGO	No
458	United Kingdom (Other)	Bilateral	No
459	United Nations Industrial Development Organization (UNIDO)	INGO	No
460	United States of America (Other)	Bilateral	Yes
461	UNSYIAH	Academic Institutions	No
462	Urgentgram	Other	No
463	USAID	Bilateral	Yes
464	USINDO	Bilateral	No
465	Vanguard Health Systems Tsunami Relief Advised Fund	Private Sector	No
466	Vision 20/20	INGO	No
467	VIVAT International Indonesia	INGO	No
468	WALHI	INGO	No
469	Walikota Banda Aceh	Other	No
470	Water Sector Belanda	Government Agency	No
471	WB (World Bank)	IFI	Yes
472	Wester Australia Newspaper	Private Sector	No
473	WFP (World Food Programme)	UN	Yes
474	WHO (World Health Organization)	UN	Yes
475	Winrock International	INGO	No
476	Wir bauen Leben	INGO	No
477	World Agroforestry Centre	INGO	Yes
478	World Care	INGO	No
479	World Heritage Center	INGO	No
480	World Relief	INGO	Yes
481	World Vision	INGO	Yes
482	YADESA	National NGO	No
483	Yagasu	National NGO	No
484	YAKKUM Emergency Unit (YEU)	National NGO	Yes
485	Yayasan Air Putih	National NGO	No
486	Yayasan Anak Bangsa	National NGO	No
487	Yayasan Bina Perdamaian Internasional Indonesia	National NGO	Yes
488	Yayasan Dian Desa	National NGO	No
489	Yayasan Ekosistem Lestari	National NGO	No
490	Yayasan Holli'ana'a	National NGO	No

CAUTION: First Data Collection Round.
Validation in progress.

RAN Database Summary Report

#	Organisation Name	Type	Access to RAN Database
491	Yayasan Ikan Tenggiri	National NGO	No
492	Yayasan Karya Banda Sejahtera	National NGO	No
493	Yayasan Kasih Peduli Masyarakat Indonesia (YKPMI)	National NGO	Yes
494	Yayasan Lembaga Ekonomi Panta Pesisir	National NGO	No
495	Yayasan MAS	National NGO	No
496	Yayasan Masyarakat Makmur Mitra Adil (MAMAMIA)	National NGO	No
497	Yayasan Mitra Dhuafa	National NGO	No
498	Yayasan Pelangi	National NGO	No
499	Yayasan Pelayanan Fajar Harapan (YFPF)	National NGO	No
500	Yayasan Pengembangan Kawasan	National NGO	No
501	Yayasan PUGAR (YADESA)	National NGO	No
502	Yayasan Rebana Indonesia	National NGO	No
503	Yayasan sosial KREASI	National NGO	Yes
504	Yayasan Tanggul Bencana di Indonesia (YTBI)	National NGO	Yes
505	Yayasan Ummul Aiman (YUA)	National NGO	No
506	YBI & Techni Service Company	National NGO	Yes
507	YIPD	National NGO	No
508	Yokohama Waterworks Bureau	INGO	No
509	Zero to One Foundation	INGO	Yes

Key: INGO - International NGO
IO - International Organisation
